
Seereon Delivery Board: Feature Guide

Santosh Nayak · 28 Sep 2026

This guide explains every feature of the board in plain words, one screen at a time, for the whole team: developers, the project manager, sales and new joiners. The screenshots come from the working prototype with dummy data. The SaaS build keeps the same screens and rules; the Technical Design has the build detail.

1. Roles and views

Everyone uses the same board, but each person sees only what their role needs. There are five roles: CEO (admin), project manager, sales, operations and employee.

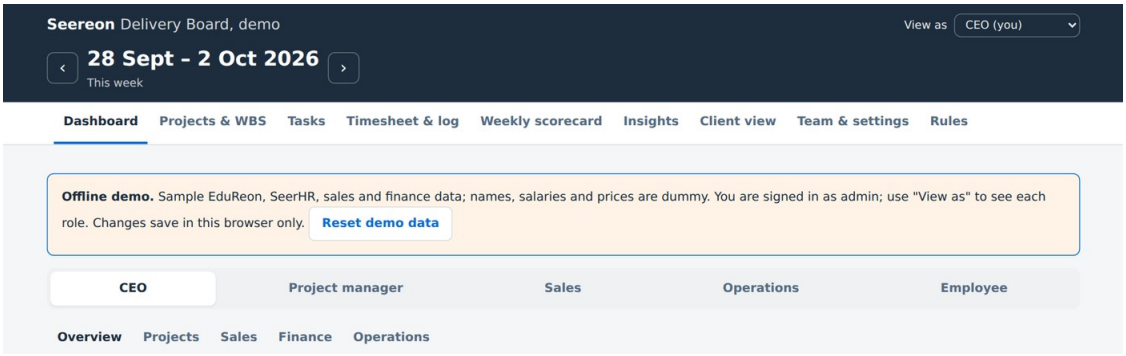


Header with the week switcher, tabs, View as control and the five dashboard views

- **Header:** the company name, the week being viewed (use the arrows to move between weeks), and the tabs you are allowed to open.
- **View as (admin only):** the CEO can switch to any role to check exactly what that person sees. In the SaaS version this mode is read-only, so nothing can be changed by accident.
- **Dashboard views:** CEO, Project manager, Sales, Operations and Employee. A salesperson lands on Sales; an employee lands on Employee and cannot open the others.

Role	Lands on	Can change	Cannot see
CEO (admin)	CEO dashboard	Everything, including settings, rates and payroll	Nothing hidden
Project manager	Project manager view	Own projects, tasks, allocation; approves team timesheets	Salaries, payroll, company finance (margins only if granted)
Sales	Sales view	Own leads and deals	Other people's pay, project costs
Operations	Operations view	Ops register,	Salaries unless

Role	Lands on	Can change	Cannot see
		openings, leave entries	granted, margins
Employee	Employee view	Own tasks' status, own timesheet, comments	Other people's timesheets, money

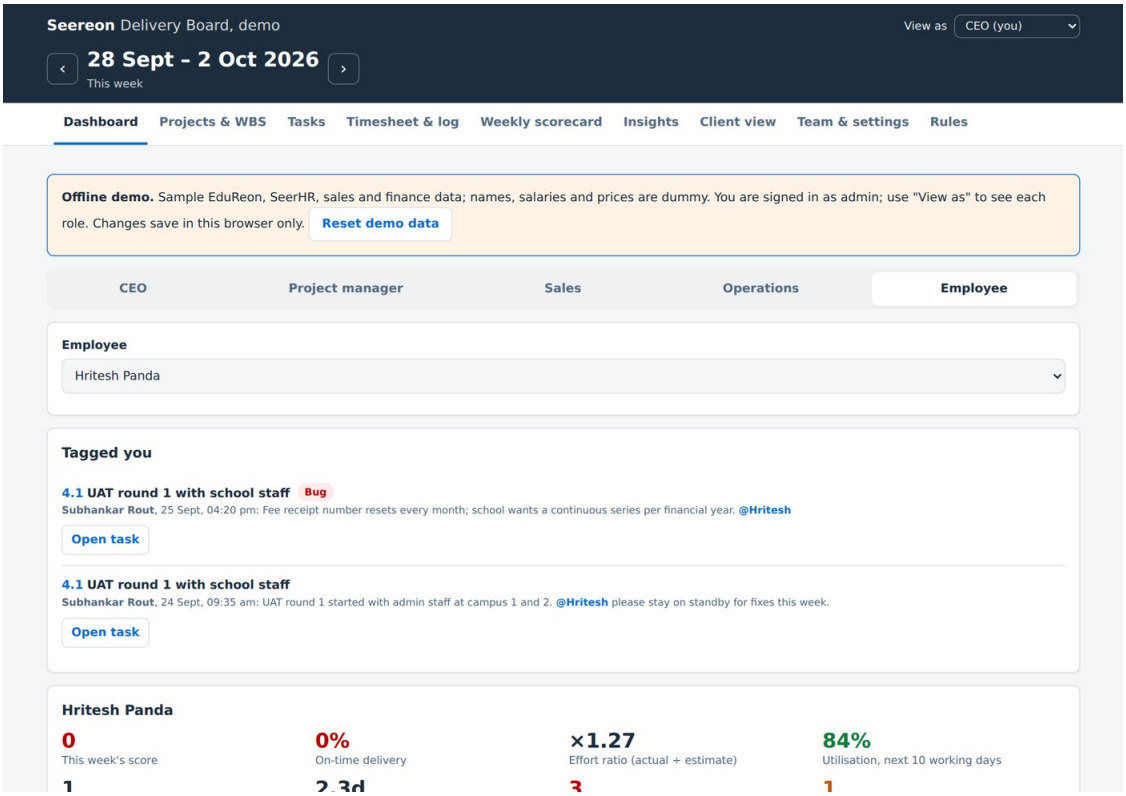


Employee view: tasks tagged to me, my week at a glance

The employee view shows only that person's world: tasks where they were mentioned or tagged, tasks they are covering for a colleague on leave, and their own delivery numbers for the week.


2. CEO dashboard: revenue first

The CEO lands on revenue, because that is the number that decides everything else. The Overview shows this month, this quarter and this financial year (April to March) side by side.

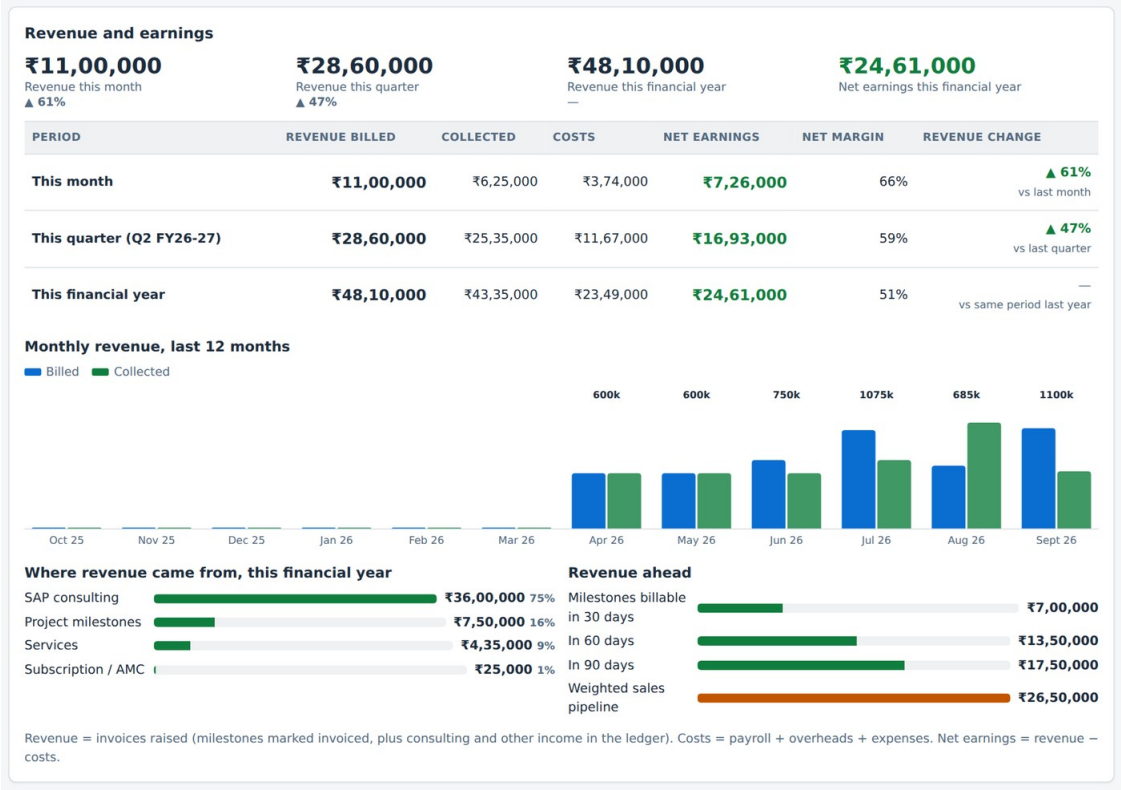

Revenue and earnings: month, quarter and year, with the 12-month chart and revenue ahead

- **Top four numbers:** revenue this month, this quarter, this financial year, and net earnings for the year. The arrow shows the change against the previous period.
- **Period table:** for each period, revenue billed, cash collected, total costs (salaries plus expenses), net earnings, net margin, and the change in revenue.
- **12-month chart:** billed and collected side by side, so a gap between invoicing and cash shows at a glance.
- **Where revenue came from:** split by stream (SAP consulting, products, services, subscriptions, AMS).
- **Revenue ahead:** milestones due but not yet invoiced, plus the weighted sales pipeline.

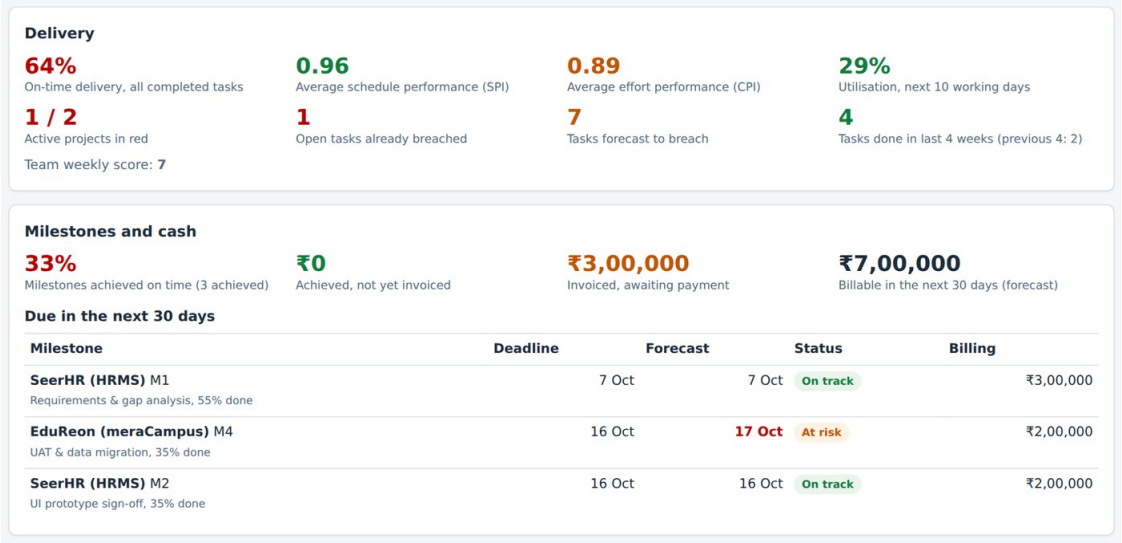


Delivery and milestone cash: health of all projects and money due in 30 days

Below revenue, **Delivery** shows how many milestones were hit on time, the schedule performance index (SPI: above 1.0 means ahead of plan), average lateness and overdue tasks. **Milestones and cash** lists milestones due in the next 30 days with their billing value, so the CEO sees which delivery dates carry money.

3. Projects: list, status, type

The Projects tab opens on a list of all projects. Click a row to open that project; click it again to close it.

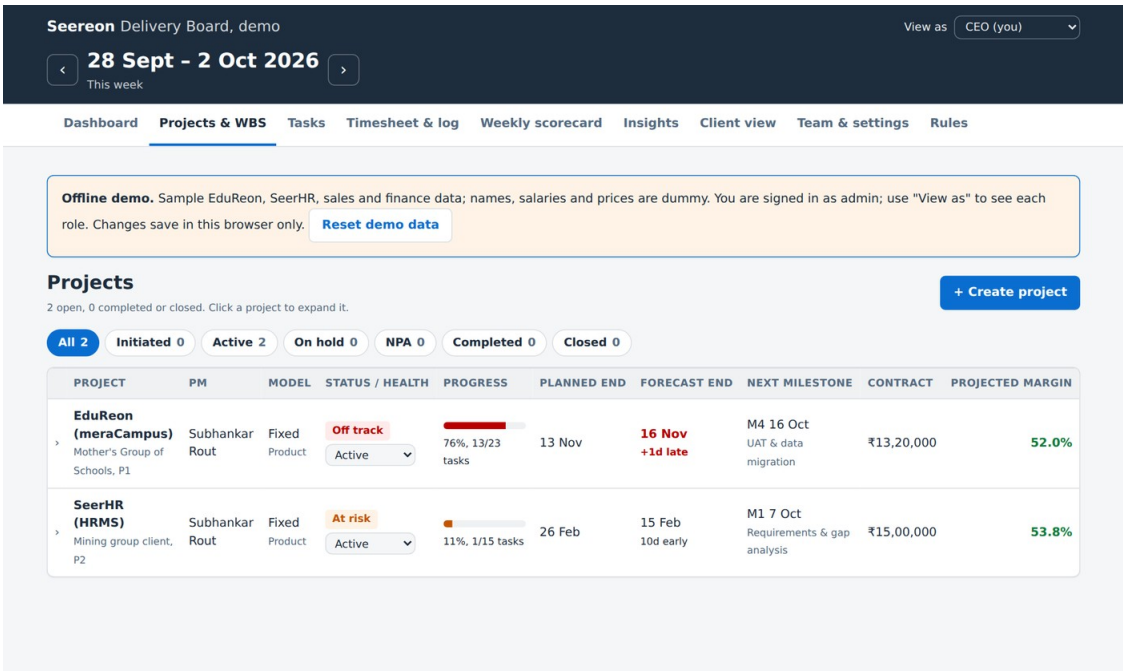


Projects list with a filter chip for each status and the Create project button

- **Status chips:** All, Initiated, Active, On hold, NPA, Completed, Closed, each with a count. Click one to see only those projects.
- **Status column:** shows health (On track, At risk, Off track) and a dropdown to change the status right from the list. Moving to On hold, NPA (non-performing asset: a client not paying or not engaging) or Closed asks for a reason; every change is kept in the project's status history.
- **Columns:** project manager, commercial model (fixed price, time and material), type, progress (% and tasks done), planned end, forecast end (red when late), next milestone, contract value and projected margin.

Status	Means
Initiated	Signed or agreed, work not started
Active	Work in progress
On hold	Paused; reason required
NPA	Client not paying or not responding; reason required
Completed	All work delivered, awaiting closure or final payment
Closed	Commercially closed; reason required

Project types: Product, Service, SaaS, AMS (annual maintenance support).

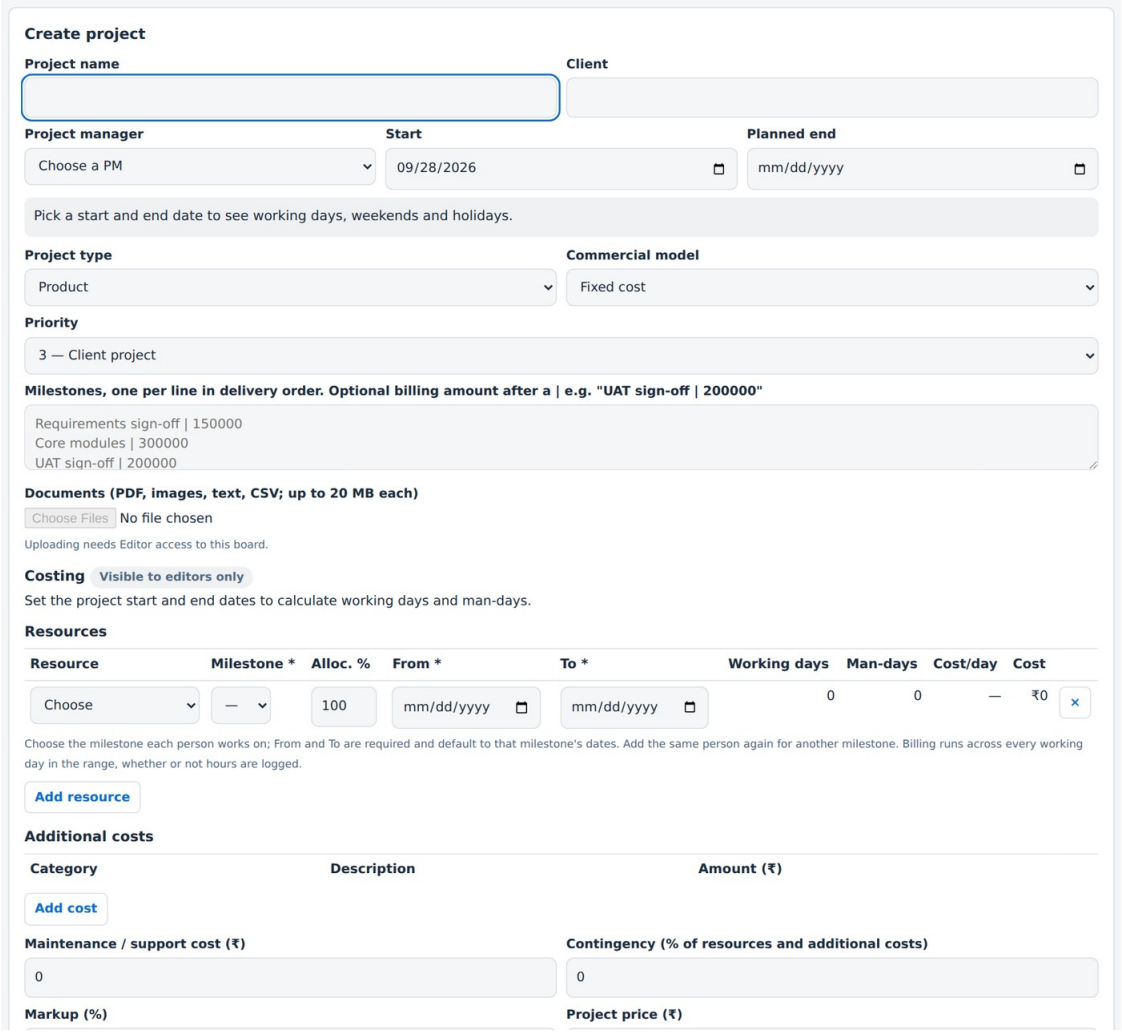


Create project form: name, client, manager, dates, type, model, milestones and costing

+ Create project opens the form: name, client, project manager, start and planned end, type, commercial model, priority, milestones with billing amounts, documents, and the costing plan. The project code is generated automatically.


4. Project page: milestones, tasks and WBS

A project is broken into milestones, and milestones into tasks. That structure is the WBS (work breakdown structure).

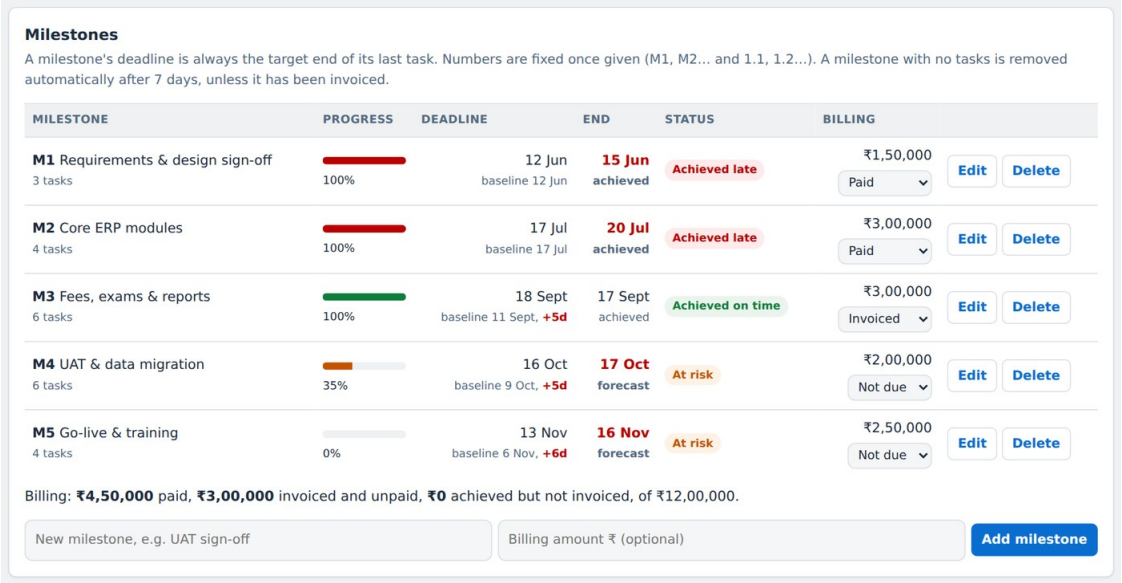

Milestones M1 to M5 with progress, deadline, status, billing, Edit and Delete

- **Automatic numbers:** milestones are numbered M1, M2, M3 in order of creation; tasks inside M2 are 2.1, 2.2, 2.3. Numbers never change and are never reused, so “task 3.4” means the same thing in every conversation.
- **Deadline and end:** a milestone’s deadline is the target end of its last task. The baseline shows the original date; red text shows the slip (for example +5d).
- **Status:** Achieved on time, Achieved late, On track, At risk.
- **Billing:** each milestone carries an amount and a billing state (Not due, Invoiced, Paid). The line below totals paid, invoiced-but-unpaid and achieved-but-not-invoiced.
- **Edit and Delete:** change a milestone’s name, dates or billing amount. A milestone that has been invoiced cannot be deleted. Deleting one moves its tasks to “No milestone”.
- **Auto-cleanup:** a milestone with no tasks for 7 days is removed automatically, unless it has been invoiced.
- **Add milestone:** type a name and optional billing amount at the bottom.

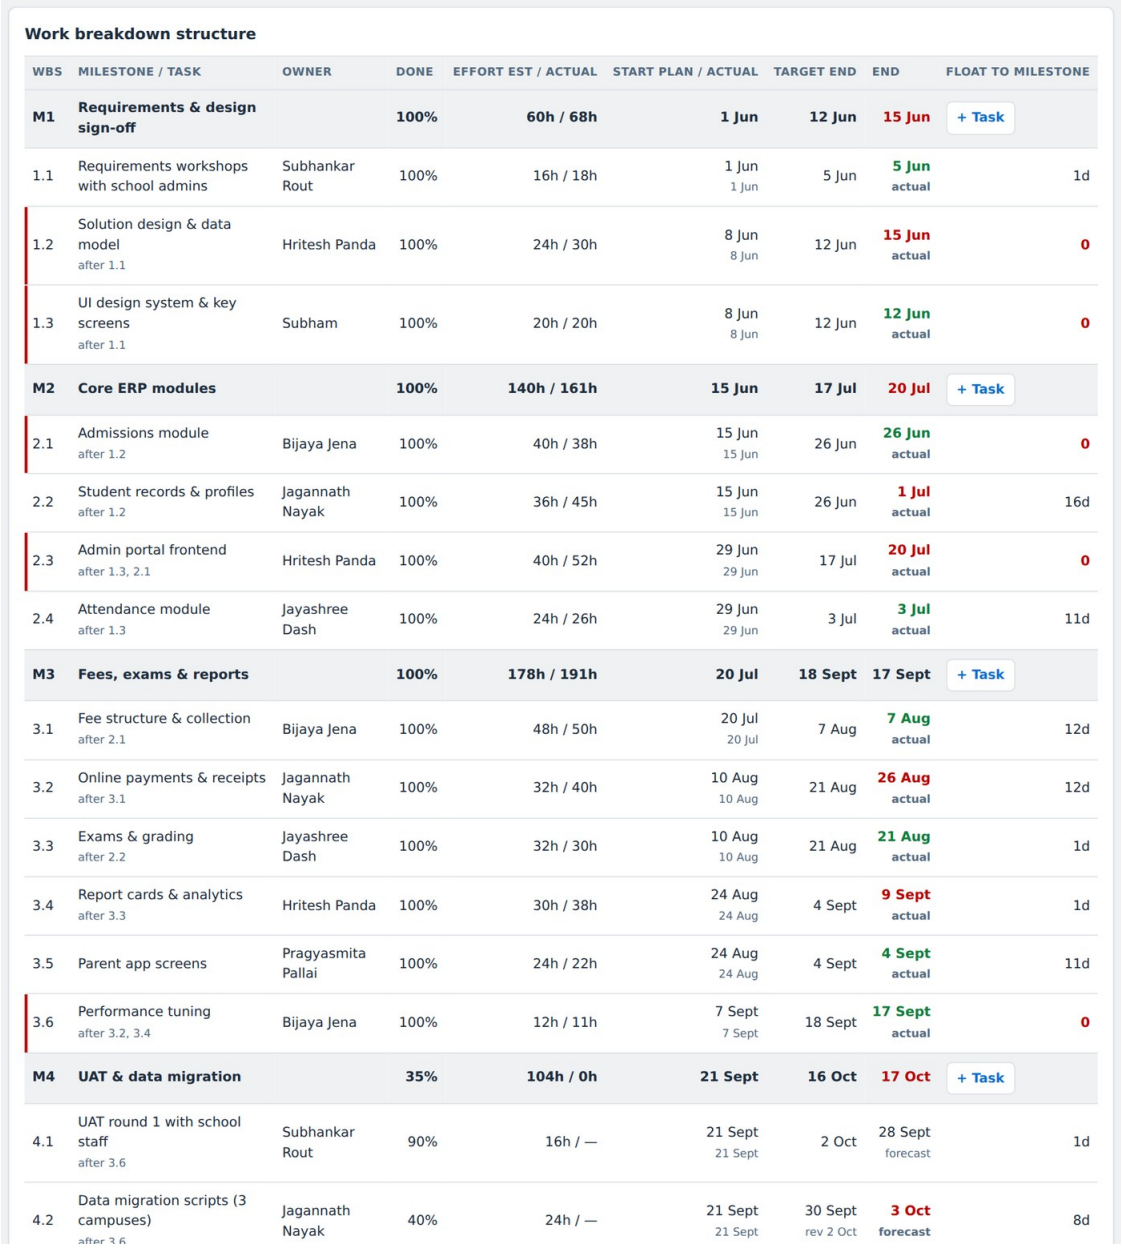

Work breakdown structure


WBS	MILESTONE / TASK	OWNER	DONE	EFFORT EST / ACTUAL	START PLAN / ACTUAL	TARGET END	END	FLOAT TO MILESTONE
M1	**Requirements & design sign-off**		**100%**	**60h / 68h**	**1 Jun**	**12 Jun**	**15 Jun**	+ Task
1.1	Requirements workshops with school admins	Subhankar Rout	100%	16h / 18h	1 Jun 1 Jun	5 Jun	**5 Jun** actual	1d
1.2	Solution design & data model after 1.1	Hritesh Panda	100%	24h / 30h	8 Jun 8 Jun	12 Jun	**15 Jun** actual	**0**
1.3	UI design system & key screens after 1.1	Subham	100%	20h / 20h	8 Jun 8 Jun	12 Jun	**12 Jun** actual	**0**
M2	**Core ERP modules**		**100%**	**140h / 161h**	**15 Jun**	**17 Jul**	**20 Jul**	+ Task
2.1	Admissions module after 1.2	Bijaya Jena	100%	40h / 38h	15 Jun 15 Jun	26 Jun	**26 Jun** actual	**0**
2.2	Student records & profiles after 1.2	Jagannath Nayak	100%	36h / 45h	15 Jun 15 Jun	26 Jun	**1 Jul** actual	16d
2.3	Admin portal frontend after 1.3, 2.1	Hritesh Panda	100%	40h / 52h	29 Jun 29 Jun	17 Jul	**20 Jul** actual	**0**
2.4	Attendance module after 1.3	Jayashree Dash	100%	24h / 26h	29 Jun 29 Jun	3 Jul	**3 Jul** actual	11d
M3	**Fees, exams & reports**		**100%**	**178h / 191h**	**20 Jul**	**18 Sept**	**17 Sept**	+ Task
3.1	Fee structure & collection after 2.1	Bijaya Jena	100%	48h / 50h	20 Jul 20 Jul	7 Aug	**7 Aug** actual	12d
3.2	Online payments & receipts after 3.1	Jagannath Nayak	100%	32h / 40h	10 Aug 10 Aug	21 Aug	**26 Aug** actual	12d
3.3	Exams & grading after 2.2	Jayashree Dash	100%	32h / 30h	10 Aug 10 Aug	21 Aug	**21 Aug** actual	1d
3.4	Report cards & analytics after 3.3	Hritesh Panda	100%	30h / 38h	24 Aug 24 Aug	4 Sept	**9 Sept** actual	1d
3.5	Parent app screens	Pragyasmita Pallai	100%	24h / 22h	24 Aug 24 Aug	4 Sept	**4 Sept** actual	11d
3.6	Performance tuning after 3.2, 3.4	Bijaya Jena	100%	12h / 11h	7 Sept 7 Sept	18 Sept	**17 Sept** actual	**0**
M4	**UAT & data migration**		**35%**	**104h / 0h**	**21 Sept**	**16 Oct**	**17 Oct**	+ Task
4.1	UAT round 1 with school staff after 3.6	Subhankar Rout	90%	16h / —	21 Sept 21 Sept	2 Oct	28 Sept forecast	1d
4.2	Data migration scripts (3 campuses) after 3.6	Jagannath Nayak	40%	24h / —	21 Sept 21 Sept	30 Sept rev 2 Oct	**3 Oct** forecast	8d

Work breakdown structure: tasks grouped by milestone, with owner, effort, dates and a + Task button per milestone

The **Work breakdown structure** lists every task under its milestone with its number, owner, effort (estimated vs actual hours), start and planned end, and float (spare days before it delays the project). **+ Task** on each milestone adds a task straight into it.


WBS import: instead of typing, paste rows from a spreadsheet or upload a CSV with the columns Milestone, Task, Owner, Estimated hours, Start, End, Complexity, Depends on, Milestone billing. **Download template** gives the exact format. **Preview** shows every row and flags errors (unknown owner, bad date, unknown dependency) before anything is saved; the import then saves all rows or none.

5. Schedule, critical path and change requests

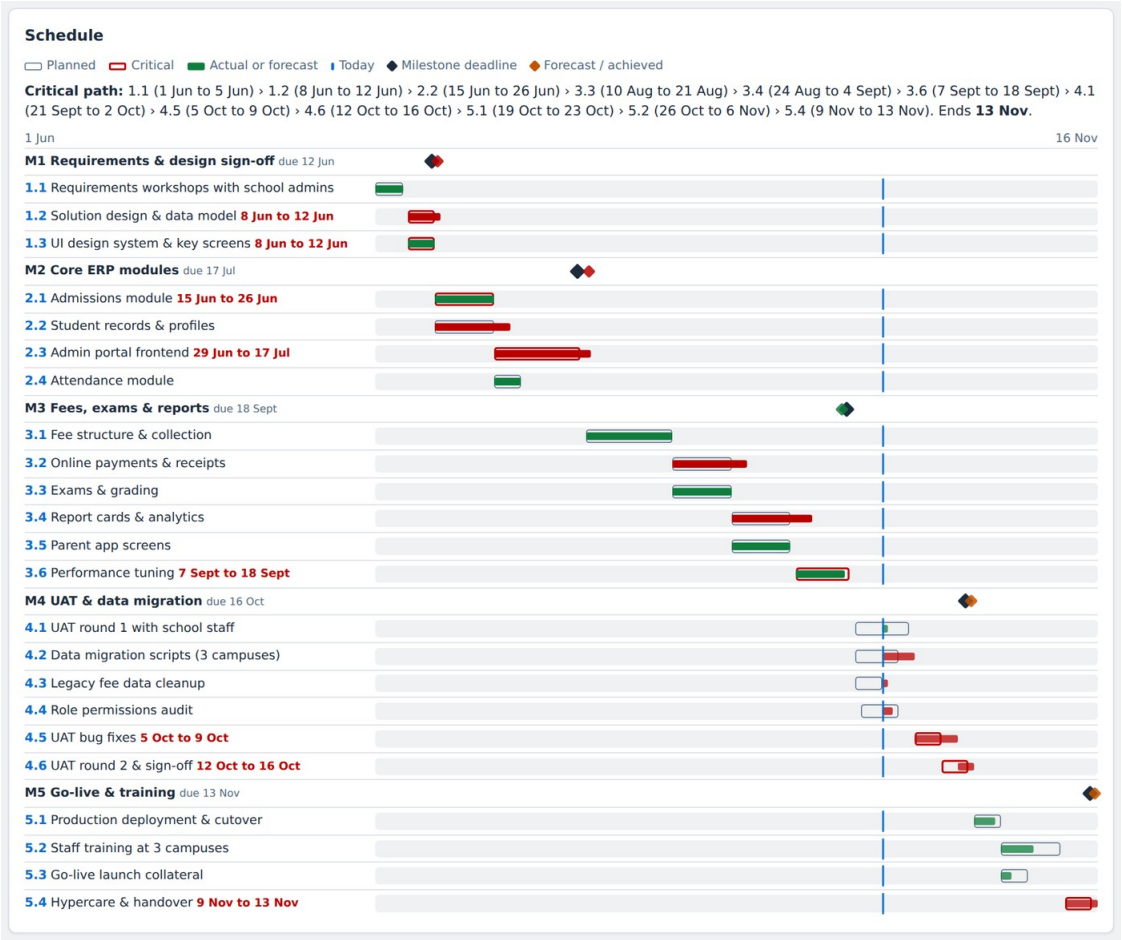


Schedule: a Gantt chart of tasks by milestone, with today's line, the baseline and critical dates

The **Schedule** is a Gantt chart: one bar per task, grouped by milestone, placed by date. Critical tasks are red; milestones are marked on their dates; the dashed line is today. The **critical path** is the longest chain of dependent tasks to the project end: any delay on it delays the whole project, so those tasks get the most attention.

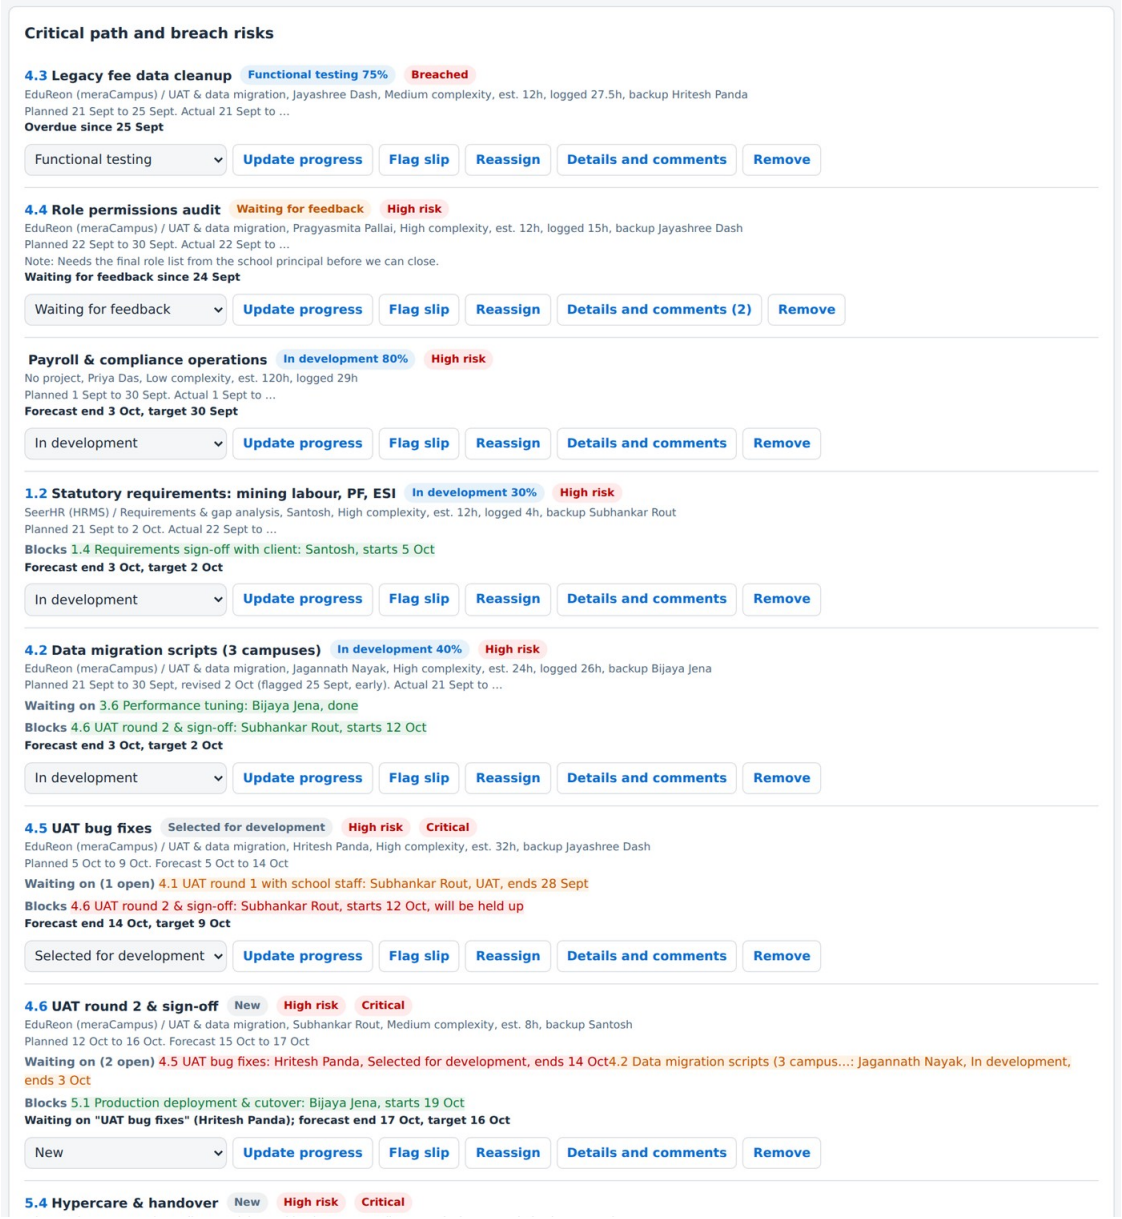

Critical path and breach risks, with actions to update progress, flag, reassign or comment

The project manager's **Critical path and breach risks** list shows each at-risk task, why it is at risk (waiting for another task, falling behind its estimate), and one-click actions: update progress, flag, reassign, or open the thread.

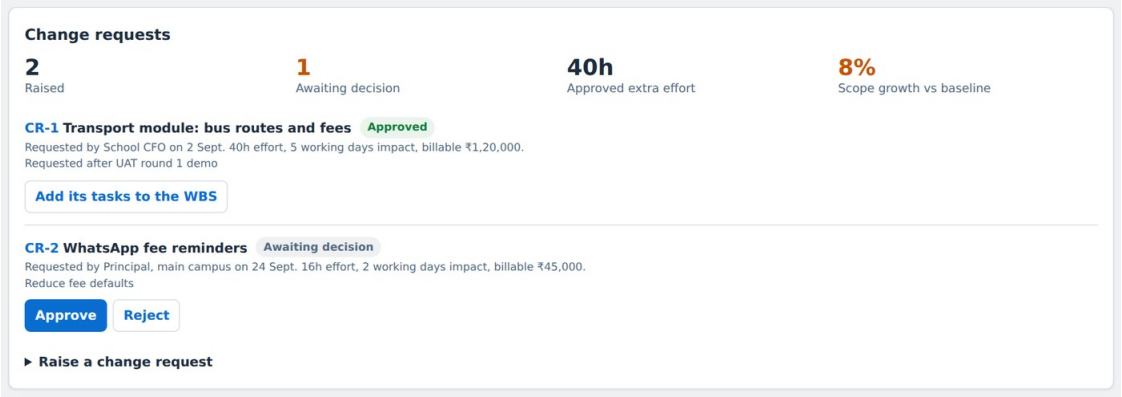


Change requests: raise, approve or reject, with effort and value

Change requests record anything the client adds after signing: title, effort in hours and value. Approving one adds its value to the contract and can add its tasks to the WBS. Nothing enters the plan without an approved change request, which protects the margin.

6. Costing, allocation and margins

Every project has a cost as well as a price. The board works out cost from the people on it and their hourly rate.

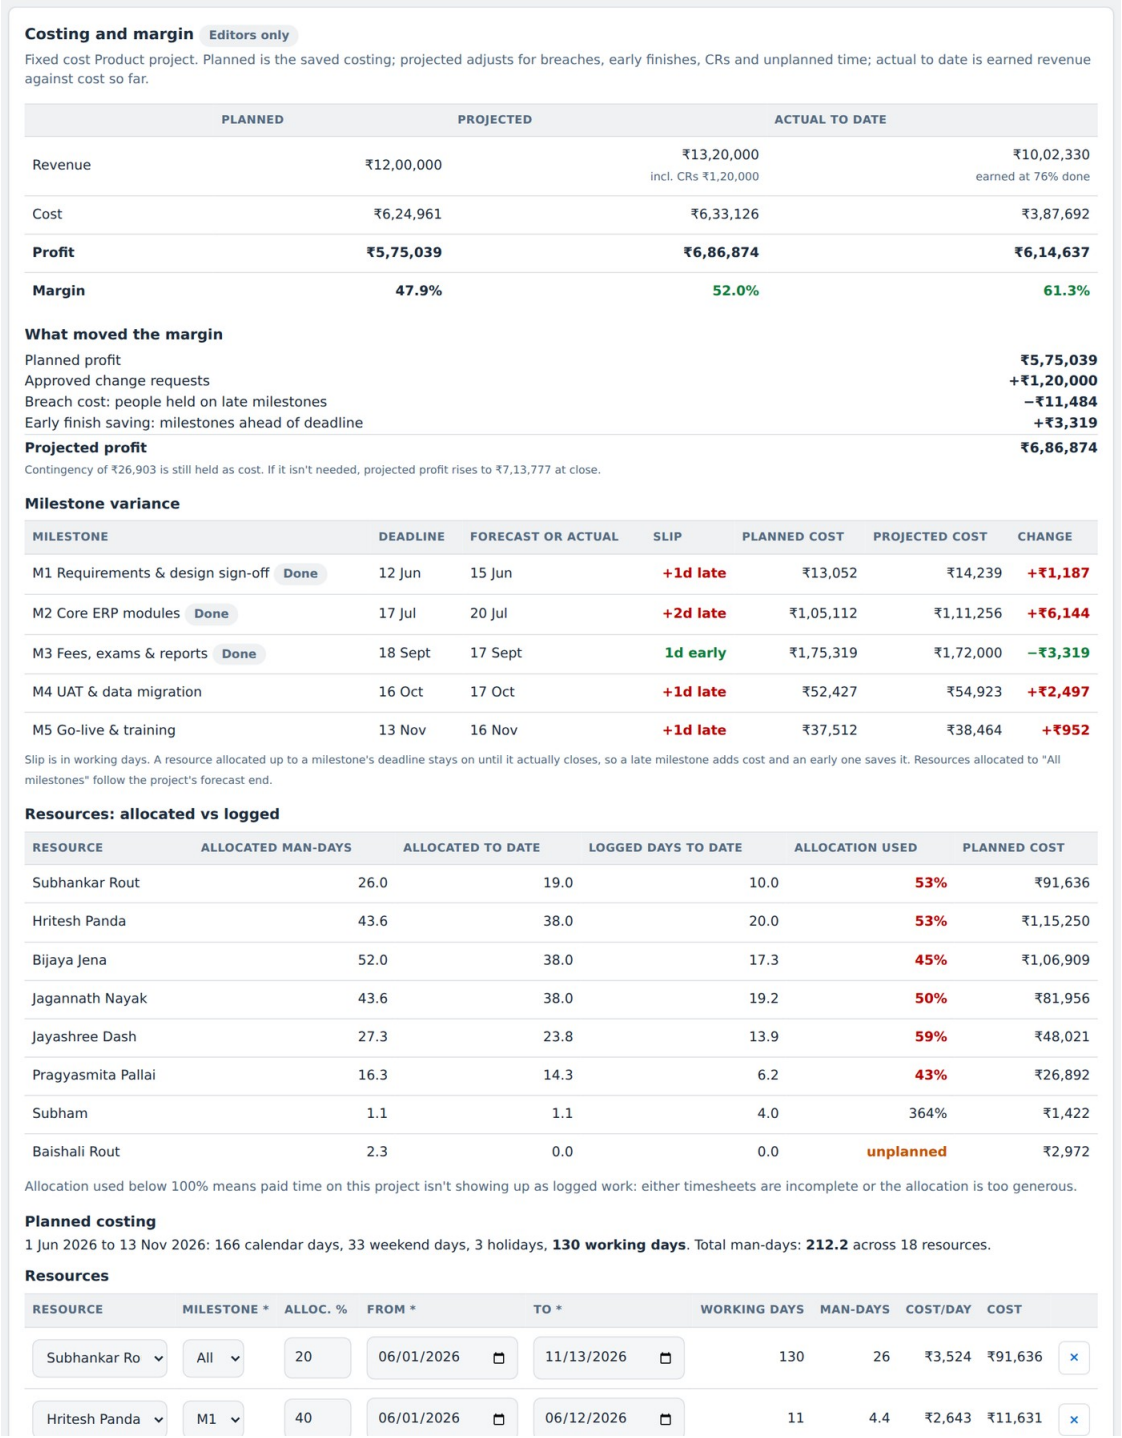

Costing and margin Editors only

Fixed cost Product project. Planned is the saved costing; projected adjusts for breaches, early finishes, CRs and unplanned time; actual to date is earned revenue against cost so far.

	PLANNED	PROJECTED	ACTUAL TO DATE
Revenue	₹12,00,000	₹13,20,000 incl. CRs ₹1,20,000	₹10,02,330 earned at 76% done
Cost	₹6,24,961	₹6,33,126	₹3,87,692
Profit	**₹5,75,039**	**₹6,86,874**	**₹6,14,637**
Margin	**47.9%**	**52.0%**	**61.3%**

What moved the margin

Planned profit	**₹5,75,039**
Approved change requests	**+₹1,20,000**
Breach cost: people held on late milestones	**−₹11,484**
Early finish saving: milestones ahead of deadline	**+₹3,319**
Projected profit	**₹6,86,874**

Contingency of ₹26,903 is still held as cost. If it isn't needed, projected profit rises to ₹7,13,777 at close.

Milestone variance

MILESTONE	DEADLINE	FORECAST OR ACTUAL	SLIP	PLANNED COST	PROJECTED COST	CHANGE
M1 Requirements & design sign-off Done	12 Jun	15 Jun	**+1d late**	₹13,052	₹14,239	**+₹1,187**
M2 Core ERP modules Done	17 Jul	20 Jul	**+2d late**	₹1,05,112	₹1,11,256	**+₹6,144**
M3 Fees, exams & reports Done	18 Sept	17 Sept	**1d early**	₹1,75,319	₹1,72,000	**−₹3,319**
M4 UAT & data migration	16 Oct	17 Oct	**+1d late**	₹52,427	₹54,923	**+₹2,497**
M5 Go-live & training	13 Nov	16 Nov	**+1d late**	₹37,512	₹38,464	**+₹952**

Slip is in working days. A resource allocated up to a milestone's deadline stays on until it actually closes, so a late milestone adds cost and an early one saves it. Resources allocated to "All milestones" follow the project's forecast end.

Resources: allocated vs logged

RESOURCE	ALLOCATED MAN-DAYS	ALLOCATED TO DATE	LOGGED DAYS TO DATE	ALLOCATION USED	PLANNED COST
Subhankar Rout	26.0	19.0	10.0	**53%**	₹91,636
Hritesh Panda	43.6	38.0	20.0	**53%**	₹1,15,250
Bijaya Jena	52.0	38.0	17.3	**45%**	₹1,06,909
Jagannath Nayak	43.6	38.0	19.2	**50%**	₹81,956
Jayashree Dash	27.3	23.8	13.9	**59%**	₹48,021
Pragyasmita Pallai	16.3	14.3	6.2	**43%**	₹26,892
Subham	1.1	1.1	4.0	364%	₹1,422
Baishali Rout	2.3	0.0	0.0	**unplanned**	₹2,972

Allocation used below 100% means paid time on this project isn't showing up as logged work: either timesheets are incomplete or the allocation is too generous.

Planned costing

1 Jun 2026 to 13 Nov 2026: 166 calendar days, 33 weekend days, 3 holidays, **130 working days**. Total man-days: **212.2** across 18 resources.

Resources

RESOURCE	MILESTONE *	ALLOC. %	FROM *	TO *	WORKING DAYS	MAN-DAYS	COST/DAY	COST	
Subhankar Ro	All	20	06/01/2026	11/13/2026	130	26	₹3,524	₹91,636	×
Hritesh Panda	M1	40	06/01/2026	06/12/2026	11	4.4	₹2,643	₹11,631	×

Costing and margin: planned, projected and actual; what moved the margin; milestone variance; resources allocated vs logged

Resource allocation by milestone. Each resource row names a person, the milestone (M1, M2, shown by code), the % of their time, and a from and to date. All four are required, so cost always lands on a milestone and a period.

Cost per hour = monthly salary (CTC) ÷ (working days in the month × minimum hours per day). Example: ₹60,000 ÷ (22 × 9) = ₹303 per hour.


Three margins:

Margin	Revenue used	Cost used	Answers
Planned	Contract value	Allocation and estimates	What did we expect to make?
Projected	Contract value	Actual so far + what's left	Where are we heading?
Actual	Invoiced amount	Approved hours only	What have we really made?

Margin vs markup. They are not the same number. Margin = profit ÷ price; markup = profit ÷ cost. If a job costs ₹1,00,000 and you charge ₹1,50,000, the markup is 50% but the margin is 33%. The board shows both side by side; decisions use margin.

Effort ratio = actual hours ÷ estimated hours. 1.0 means on estimate; 1.3 means the work took 30% longer than planned. It is shown per task, milestone and project, and anything above 1.2 is flagged.

What moved the margin explains the gap between planned and projected (for example: approved change requests, extra hours on a late milestone). **Milestone variance** shows each milestone's planned cost against its forecast. **Resources: allocated vs logged** compares each person's planned hours to the hours they actually logged.

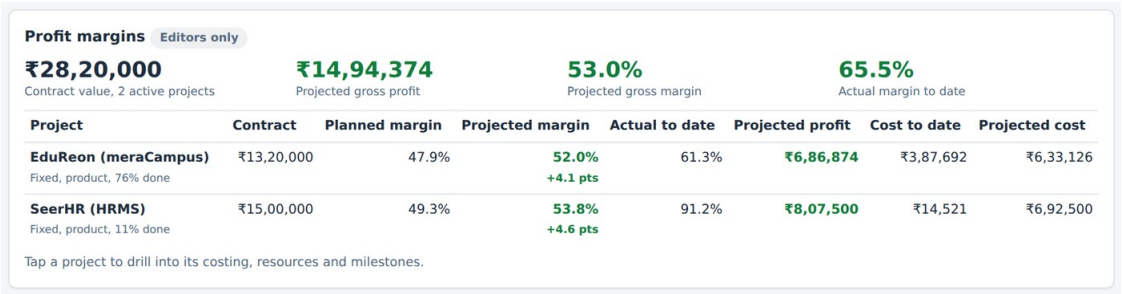

CEO view of profit margins across all projects

The CEO sees the same numbers for every project in one table. Margins are visible only to the CEO and anyone given the margins permission.

7. Tasks: owners, dependencies, backup and threads

The Tasks tab lists every task with filters by person, project and status. Each task has:


- **One owner** who is accountable, and optionally a **backup** who covers it when the owner is on leave. On leave days the task appears in the backup's "Covering" list and they can log time on it.
- **Estimated hours, start and due date, complexity** (low, medium, high). Complexity feeds estimation accuracy in Insights.

- **Status:** To do, In progress, Blocked, In review, Done.
- **Depends on:** other tasks that must finish first. A task cannot be started while something it depends on is still open; the board names the blocking task and its owner, so the conversation goes to the right person.
- **Thread:** comments on the task. Typing @name mentions a person; they get a notification and see it under “Tagged you” on their dashboard.

Dependency chains are what the critical path (section 5) is built from, so setting dependencies correctly is what makes the forecast dates trustworthy.

8. Timesheet and daily update


Time is logged once a week, against tasks and activities. Task hours become the task’s actual hours and its cost, so the timesheet feeds margins and payroll.

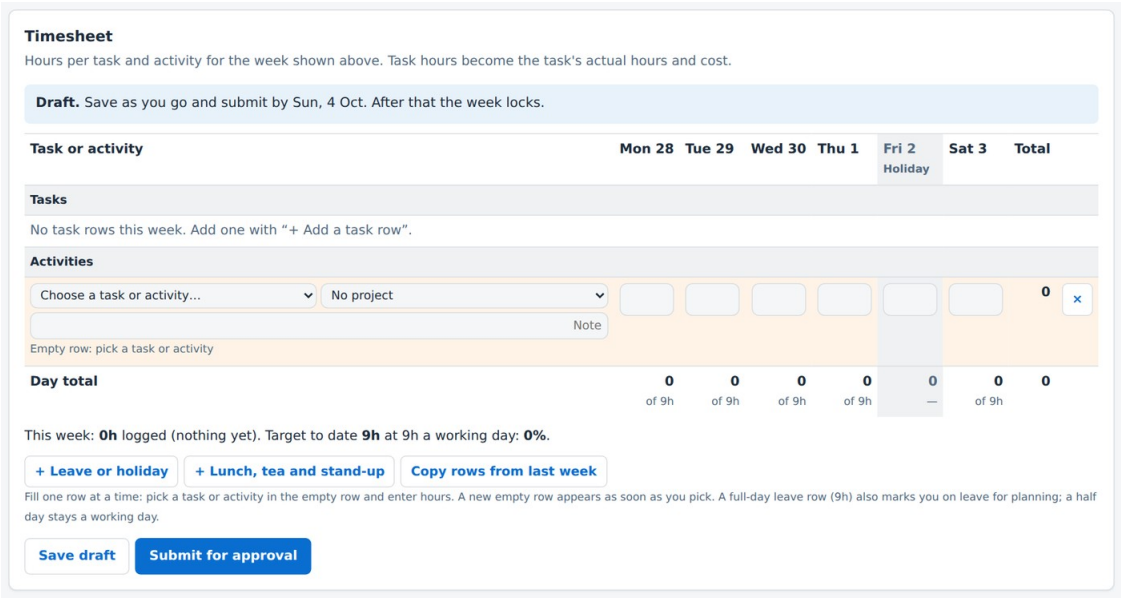

Timesheet: one empty row to fill, days of the week with the holiday greyed, day totals against 9 hours, Save draft and Submit for approval

- **One row at a time:** there is always one empty row. Pick a task or activity and enter hours; a new empty row appears as soon as you pick. Rows with no hours disappear.
- **Days:** Monday to Saturday for the week in the header. Holidays and weekly offs are greyed and marked.
- **Day total:** each day shows hours logged against the minimum (9 hours by default). Short days are highlighted.
- **Quick rows: + Leave or holiday** (a full-day leave also marks you as on leave for planning; half-day is allowed), **+ Lunch, tea and stand-up**, and **Copy rows from last week**.
- **Save draft** keeps your work. **Submit for approval** sends the week to your manager and makes it read-only for you.

- **Weekly lock:** the banner shows the deadline ("submit by Sun, 4 Oct"). An unsubmitted week locks when it ends. Only your manager or the CEO can unlock it, for a set number of days, after you request it with a reason.

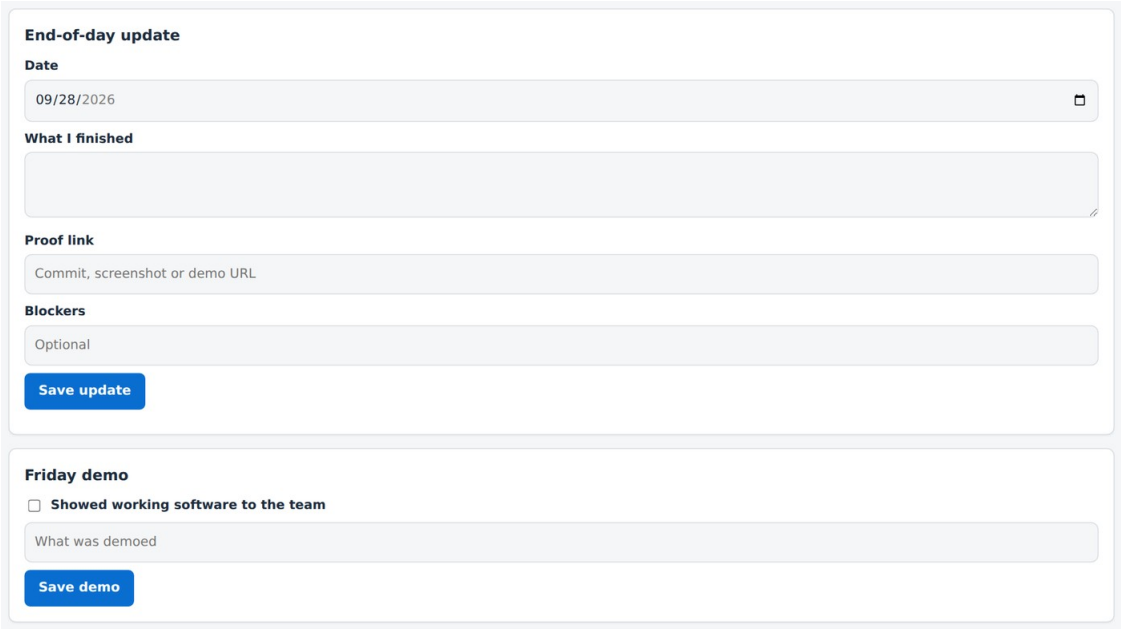


End-of-day update with a proof link, and the Friday demo check

End-of-day update: what you finished, a proof link (a commit, a document, a screenshot), and any blocker. No proof, no progress. **Friday demo** records whether you showed working software to the team that week.

9. Approvals and the manager's approval KPI

Every submitted week goes to the person's manager (their "reports to"). The manager has 2 working days to approve or reject it.

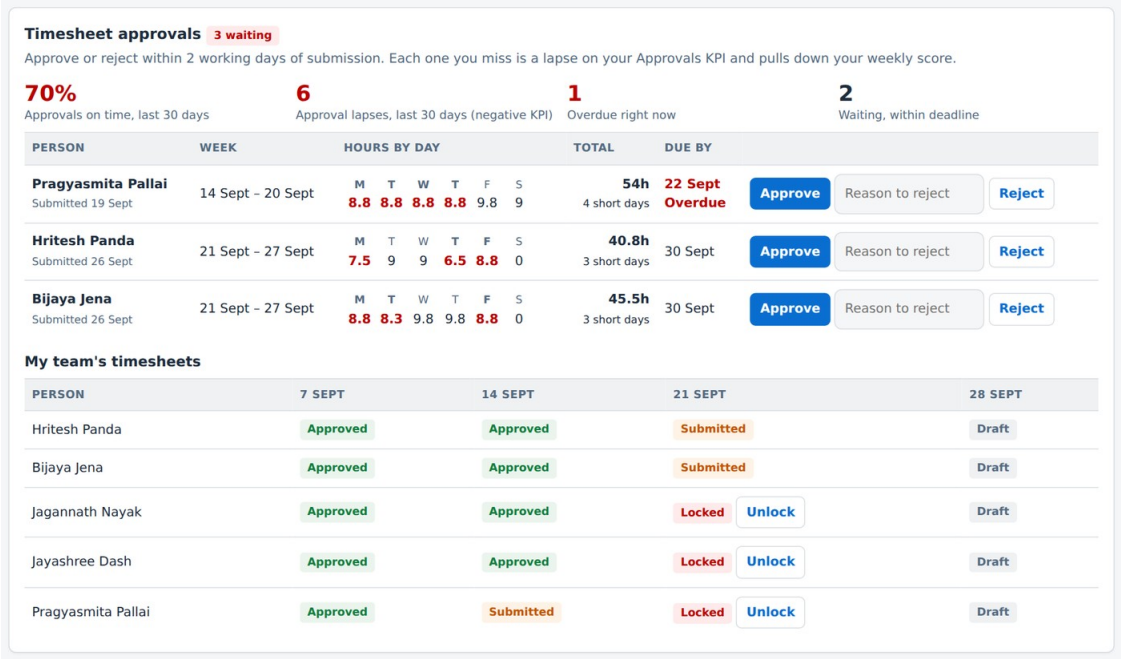


Timesheet approvals: 3 waiting, the approval KPI, hours by day with short days in red, Approve and Reject with reason, and the team's week-by-week status

- **KPI strip:** approvals on time in the last 30 days, approval lapses (a negative KPI: each approval made late or still waiting past the deadline counts against the manager), overdue right now, and waiting within the deadline.
- **Waiting list:** each week shows hours per day (short days in red), the total, and the due date. Overdue items turn red.
- **Approve** or **Reject**; rejecting needs a reason, and the week goes back to the person to fix.
- **My team's timesheets:** four weeks per person, coloured by status (Approved, Submitted, Locked, Draft). **Unlock** reopens a locked week for the person.
- **Delegation:** a manager going on leave can hand their approvals to someone else for a date range (see section 16).

The top person (the CEO) has no manager, so their weeks are approved automatically.

10. Payroll: pay for approved days

Payroll turns approved timesheets into the amount to pay each person for a month. It is visible to the CEO only.

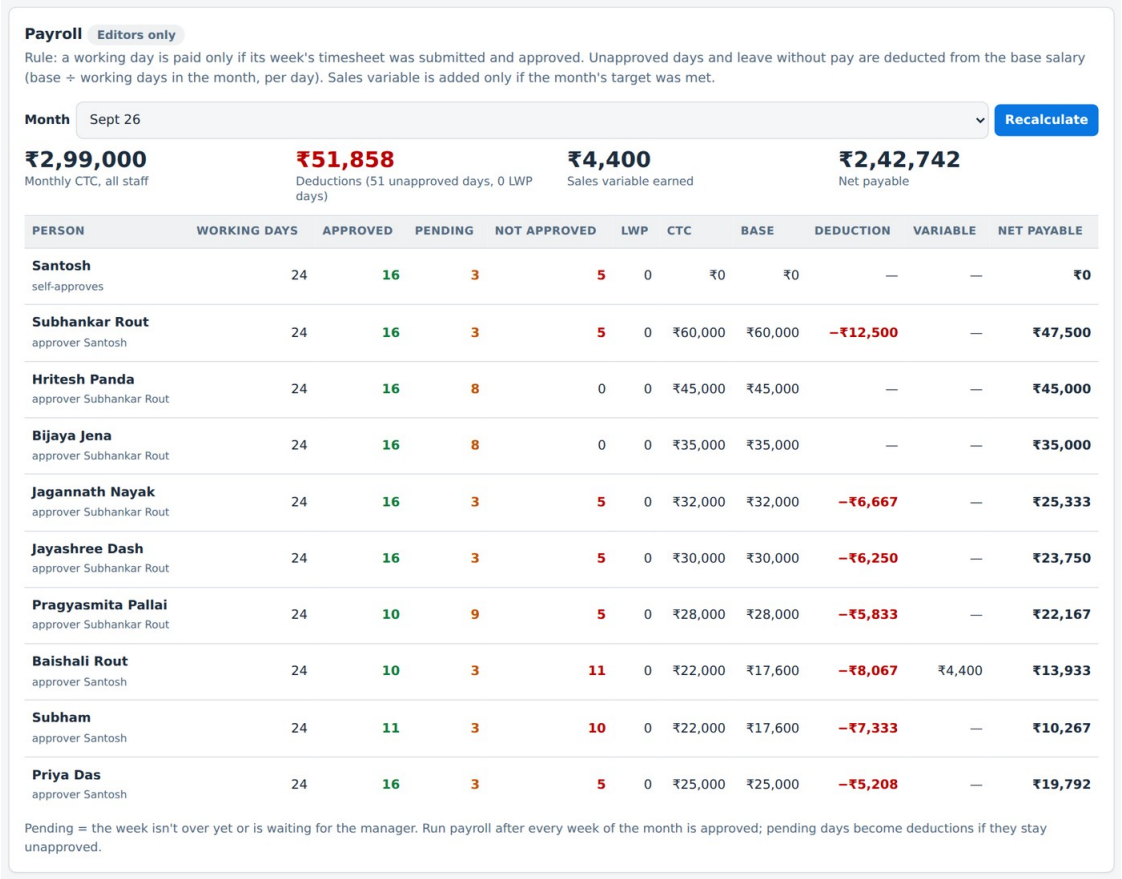

Payroll Editors only

Rule: a working day is paid only if its week's timesheet was submitted and approved. Unapproved days and leave without pay are deducted from the base salary (base ÷ working days in the month, per day). Sales variable is added only if the month's target was met.

Month: Sept 26 — Recalculate

₹2,99,000	₹51,858	₹4,400	₹2,42,742
Monthly CTC, all staff	Deductions (51 unapproved days, 0 LWP days)	Sales variable earned	Net payable

PERSON	WORKING DAYS	APPROVED	PENDING	NOT APPROVED	LWP	CTC	BASE	DEDUCTION	VARIABLE	NET PAYABLE
Santosh self-approves	24	16	3	5	0	₹0	₹0	—	—	**₹0**
Subhankar Rout approver Santosh	24	16	3	5	0	₹60,000	₹60,000	**−₹12,500**	—	**₹47,500**
Hritesh Panda approver Subhankar Rout	24	16	8	0	0	₹45,000	₹45,000	—	—	**₹45,000**
Bijaya Jena approver Subhankar Rout	24	16	8	0	0	₹35,000	₹35,000	—	—	**₹35,000**
Jagannath Nayak approver Subhankar Rout	24	16	3	5	0	₹32,000	₹32,000	**−₹6,667**	—	**₹25,333**
Jayashree Dash approver Subhankar Rout	24	16	3	5	0	₹30,000	₹30,000	**−₹6,250**	—	**₹23,750**
Pragyasmita Pallai approver Subhankar Rout	24	10	9	5	0	₹28,000	₹28,000	**−₹5,833**	—	**₹22,167**
Baishali Rout approver Santosh	24	10	3	11	0	₹22,000	₹17,600	**−₹8,067**	₹4,400	**₹13,933**
Subham approver Santosh	24	11	3	10	0	₹22,000	₹17,600	**−₹7,333**	—	**₹10,267**
Priya Das approver Santosh	24	16	3	5	0	₹25,000	₹25,000	**−₹5,208**	—	**₹19,792**

Pending = the week isn't over yet or is waiting for the manager. Run payroll after every week of the month is approved; pending days become deductions if they stay unapproved.


Payroll for a month: working days, approved and unapproved days, leave without pay, deduction, sales variable and net pay per person

- Pick the month and click **Calculate payroll**.
- For each person: working days in the month, days in approved weeks, unapproved days, leave without pay, the deduction, sales variable earned, and net pay.
- **Deduction** = monthly base ÷ working days in the month × (unapproved days + leave-without-pay days).
- **Sales variable** is added only when that month's sales target was met in full.
- Anyone with unsubmitted or unapproved weeks is flagged before you pay, so you can chase the approval first.
- The SaaS version adds a CSV export for the bank or the accountant.

In the SaaS version, deducting unapproved days is a company setting (off by default for new customers), because withholding pay is a legal decision each company should make knowingly. The board computes the payable amount only; PF, ESI and TDS are out of scope for v1.


11. Sales: leads, pipeline and the activity trail

Every deal is traceable from first contact to cash: who created it, every stage it moved through and when, and every call, meeting and proposal along the way.

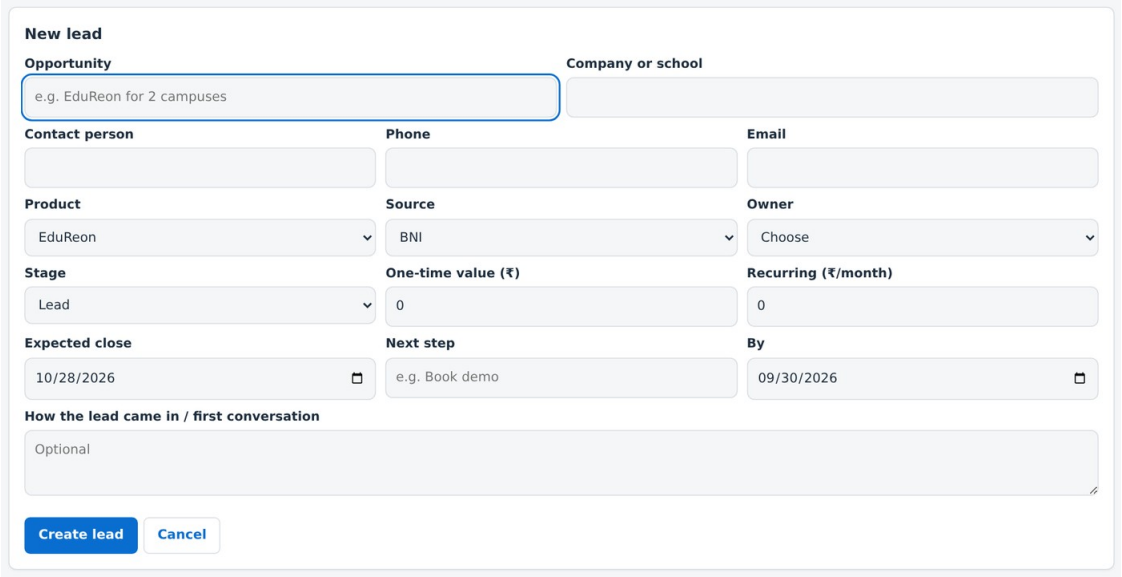

New lead form: opportunity, company, contact, product, source, owner, stage, value, recurring value, expected close and next step

+ New lead creates a lead by hand: opportunity name, company, contact person, phone, email, product, source (referral, BNI, website, cold call, event, partner), owner, stage, one-time value, monthly recurring value, expected close date, the next step and its date, and how the lead came in.

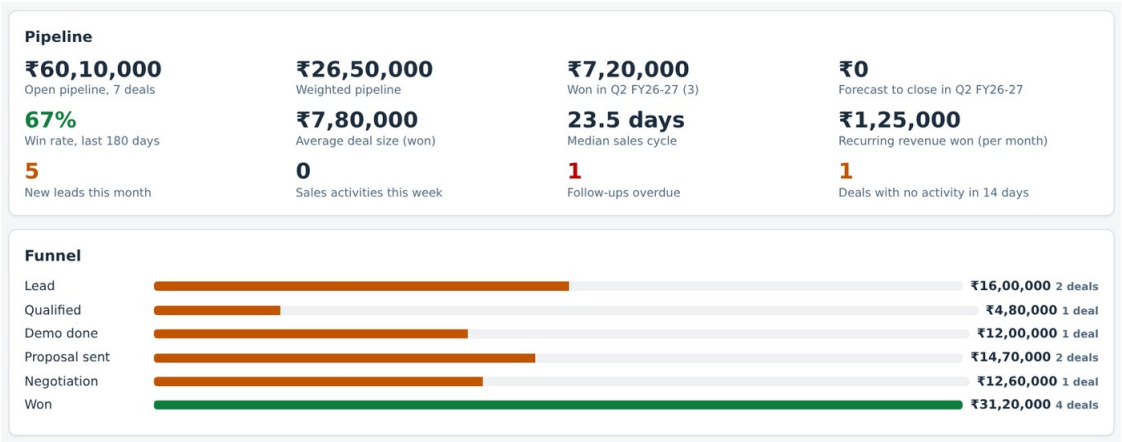

Pipeline: open value, weighted value, win rate, deals by stage and the funnel

Pipeline shows open value, weighted value (each deal's value × its stage's chance of closing), win rate, average days to close, and the funnel by stage: Lead, Qualified, Demo, Proposal, Negotiation, Won, Lost. Moving a deal to Lost asks for a reason; Won records the date and can create a project.

Sales activity log, last 30 days

Everyone (39)


DATE	WHO	DEAL	WHAT	DETAIL
25 Sept	Baishali Rout	EduReon for Coastal Engineering College Coastal Engineering College	Email	Sent intro deck
24 Sept	Baishali Rout	SeerHR for Eastern Steel Castings Eastern Steel Castings	WhatsApp	Shared SeerHR one-pager
23 Sept	Baishali Rout	EduReon for Kalinga Public School Kalinga Public School	Call	Principal wants fee module walkthrough
23 Sept	Santosh	SAP ABAP & CPI support retainer Global manufacturer (Germany)	Stage	Demo done → Proposal sent
22 Sept	Santosh	EduReon for Green Valley Academy (3 campuses) Green Valley Academy	Meeting	Trustee asked for 10% discount
22 Sept	Baishali Rout	EduReon for Coastal Engineering College Coastal Engineering College	Call	Registrar interested
22 Sept	Baishali Rout	EduReon for Coastal Engineering College Coastal Engineering College	New lead	Cold outreach
21 Sept	Baishali Rout	SeerHR for Eastern Steel Castings Eastern Steel Castings	Call	BNI referral, first call
21 Sept	Baishali Rout	SeerHR for Eastern Steel Castings Eastern Steel Castings	New lead	BNI

Sales activity log for the last 30 days: date, salesperson, deal, activity type and note

The **activity log** lists every stage change and activity in the last 30 days, by person and deal. A deal with no activity for 14 days is flagged as stale.


12. Sales cost, performance and pay

Sales is judged on what it costs against what it brings in, per person and per period.

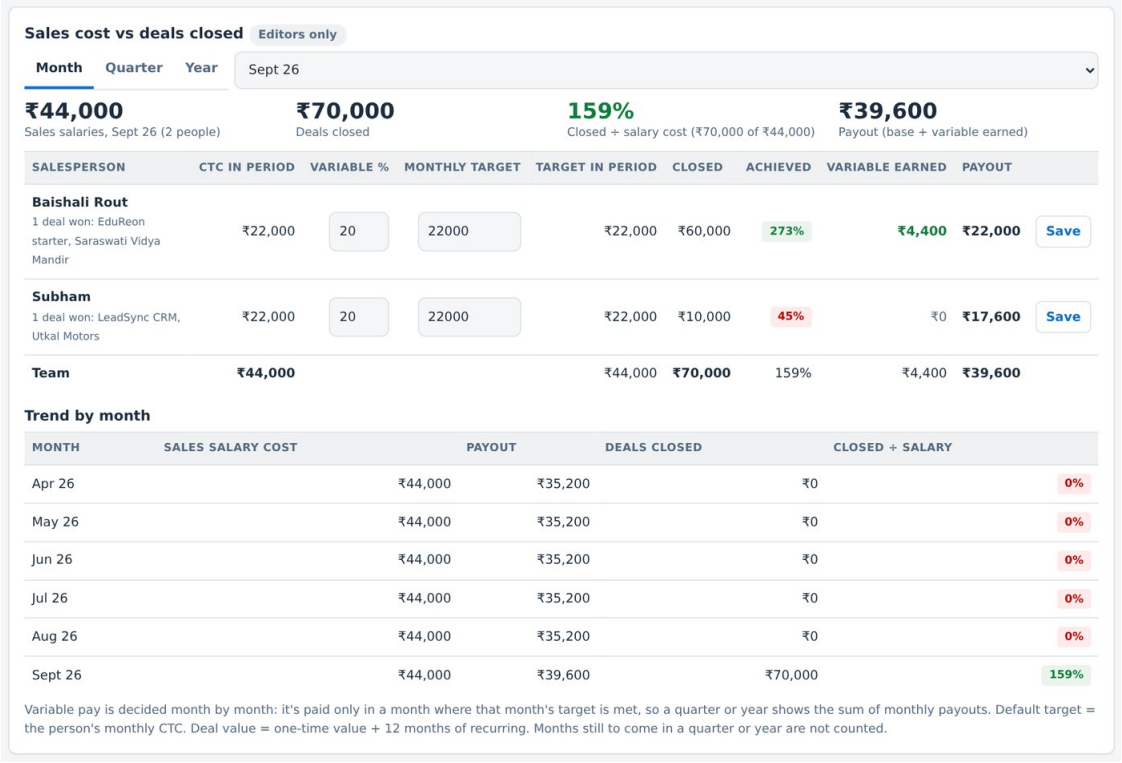

Sales cost vs deals closed: switch by month, quarter or year; base and variable pay per salesperson; target, achieved and payout; trend by month

- **Month, Quarter, Year** switch the period.
- **Sales cost** = base salary + variable pay earned. **Deals closed** = value of deals won in the period. The ratio shows how many rupees of sales each rupee of sales cost produced.
- **Base and variable:** each salesperson's pay splits into a fixed base and a variable part (20% of CTC by default). Their monthly target defaults to their monthly CTC.
- **Variable is earned only at 100% of target.** At 95% of target, only the base is paid. Example: CTC ₹50,000, variable 20% → base ₹40,000, variable ₹10,000. Achieved 95% → pay ₹40,000. Achieved 100% → pay ₹50,000.
- **Trend by month:** sales cost against deals closed for each month.

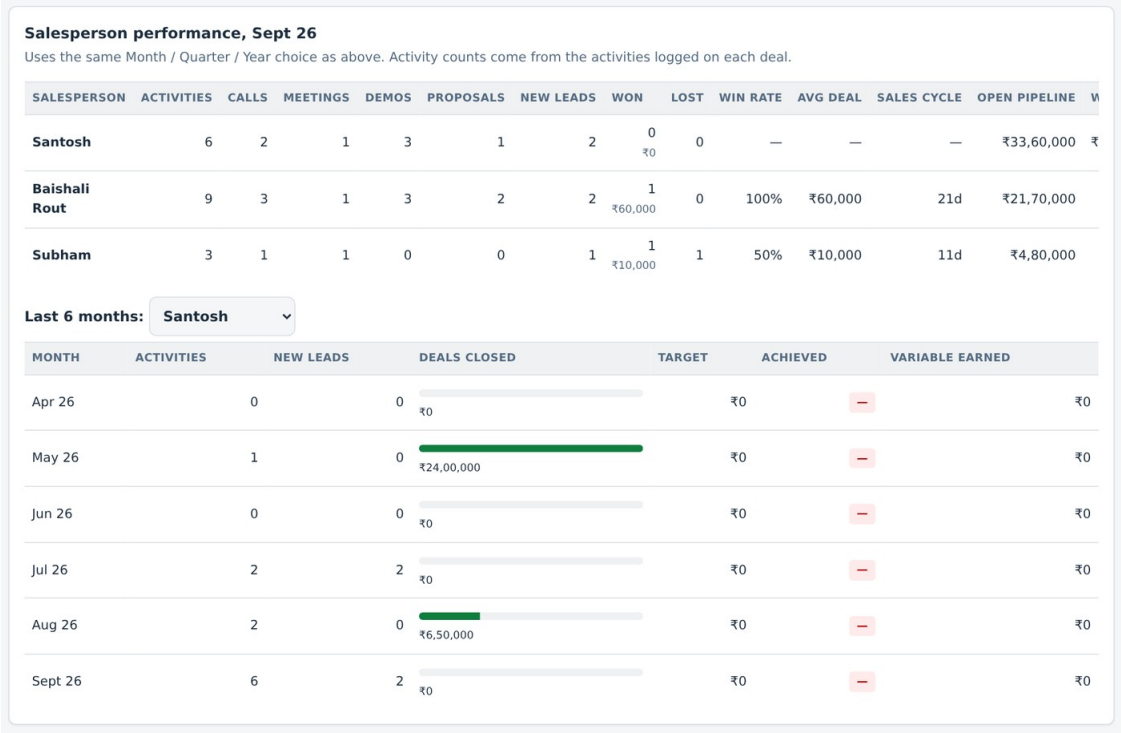

Salesperson performance, Sept 26

Uses the same Month / Quarter / Year choice as above. Activity counts come from the activities logged on each deal.

SALESPERSON	ACTIVITIES	CALLS	MEETINGS	DEMOS	PROPOSALS	NEW LEADS	WON	LOST	WIN RATE	AVG DEAL	SALES CYCLE	OPEN PIPELINE	W
Santosh	6	2	1	3	1	2	0 ₹0	0	—	—	—	₹33,60,000	₹
Baishali Rout	9	3	1	3	2	2	1 ₹60,000	0	100%	₹60,000	21d	₹21,70,000	
Subham	3	1	1	0	0	1	1 ₹10,000	1	50%	₹10,000	11d	₹4,80,000	

Last 6 months: Santosh

MONTH	ACTIVITIES	NEW LEADS	DEALS CLOSED	TARGET	ACHIEVED	VARIABLE EARNED
Apr 26	0	0	₹0	₹0	—	₹0
May 26	1	0	₹24,00,000	₹0	—	₹0
Jun 26	0	0	₹0	₹0	—	₹0
Jul 26	2	2	₹0	₹0	—	₹0
Aug 26	2	0	₹6,50,000	₹0	—	₹0
Sept 26	6	2	₹0	₹0	—	₹0

Salesperson performance: activities, calls, meetings, demos, proposals, won, lost, win rate, average deal, cycle days and open pipeline

Individual performance gives one row per salesperson for the chosen period: activities logged, calls, meetings, demos, proposals, deals won and lost, win rate, average deal size, days from lead to won, and open pipeline. Below it, each person's last six months show target against achieved.

13. Finance: P&L and ledger




Monthly P&L, last 6 months

Month	Billed	Collected	Payroll	Other costs	Net (billed − costs)
Apr 26	₹6,00,000	₹6,00,000	₹3,19,000	₹75,000	**₹2,06,000**
May 26	₹6,00,000	₹6,00,000	₹3,19,000	₹75,000	**₹2,06,000**
Jun 26	₹7,50,000	₹6,00,000	₹3,19,000	₹75,000	**₹3,56,000**
Jul 26	₹10,75,000	₹7,50,000	₹2,99,000	₹1,20,000	**₹6,56,000**
Aug 26	₹6,85,000	₹11,60,000	₹2,99,000	₹75,000	**₹3,11,000**
Sept 26	₹11,00,000	₹6,25,000	₹2,99,000	₹75,000	**₹7,26,000**

Payroll uses current CTCs for everyone employed in that month.

Monthly profit and loss for the last 6 months: billed, collected, payroll, other costs, net


Monthly P&L shows, for each of the last six months, what was billed, what was collected, payroll cost, other costs, and net (billed minus costs). It updates as invoices, payments and expenses are recorded.

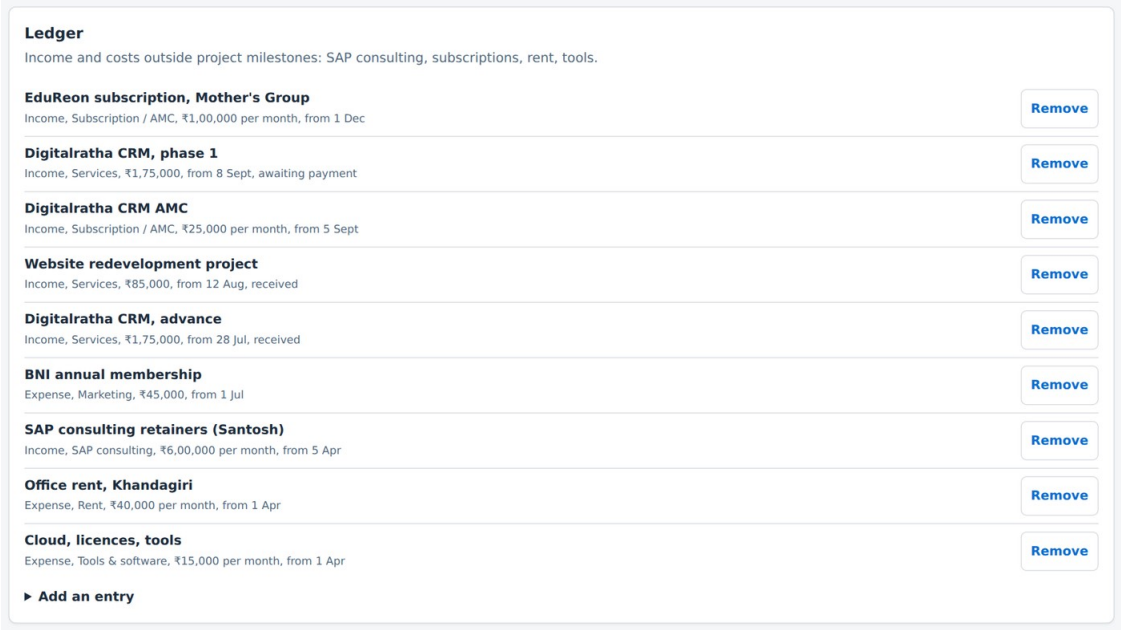

Ledger: income and expense entries, recurring ones marked, with add and remove


The **Ledger** records income and expenses that do not come from project milestones: subscriptions, consulting retainers, rent, software. An entry can repeat monthly until an end date, so a ₹6,00,000 monthly retainer is entered once and appears in every month's revenue. Milestone invoices add their income automatically.

14. Project manager and operations dashboards

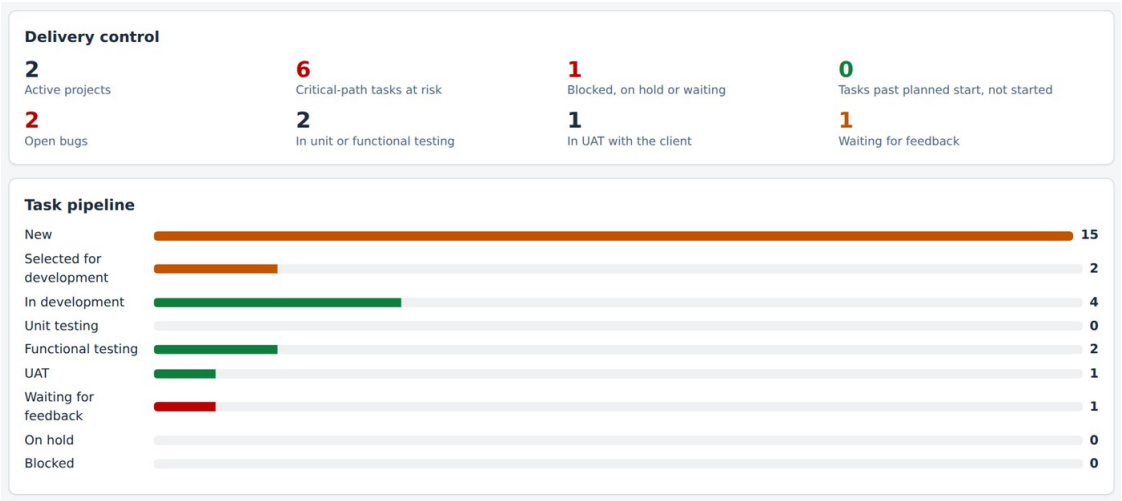


Project manager view: delivery control numbers and the task pipeline by status

The **Project manager** view starts with delivery control: active projects, critical tasks at risk, blocked or waiting tasks, tasks that should have started, tasks with no estimate, and scheduling conflicts. The task pipeline shows how many tasks sit in each status, so a pile-up in "In review" or "Blocked" is obvious.

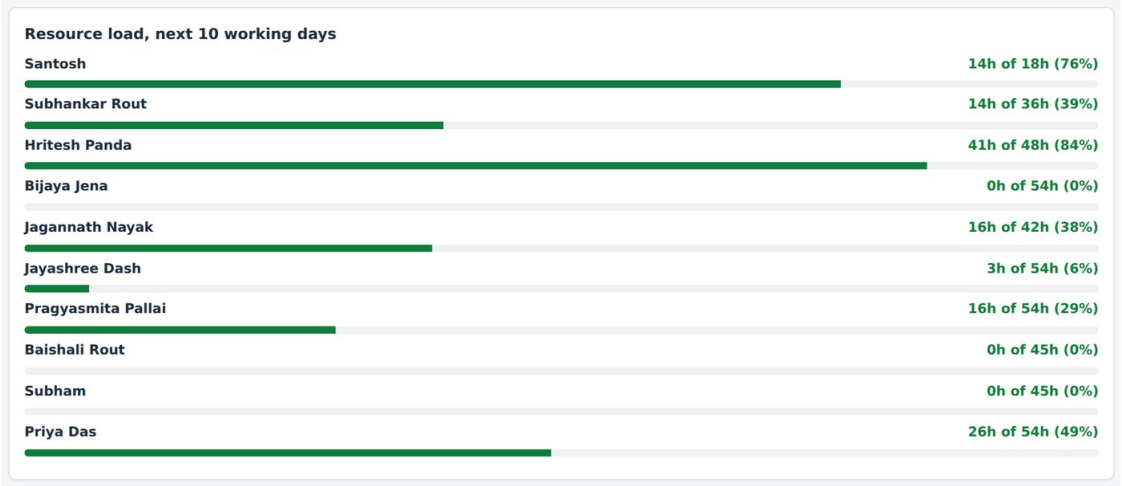

Resource load for the next 10 working days: each person's booked hours against capacity


Resource load shows each person's booked hours against their capacity for the next 10 working days. Over 100% means someone is double-booked; well under means spare capacity to pull work forward.

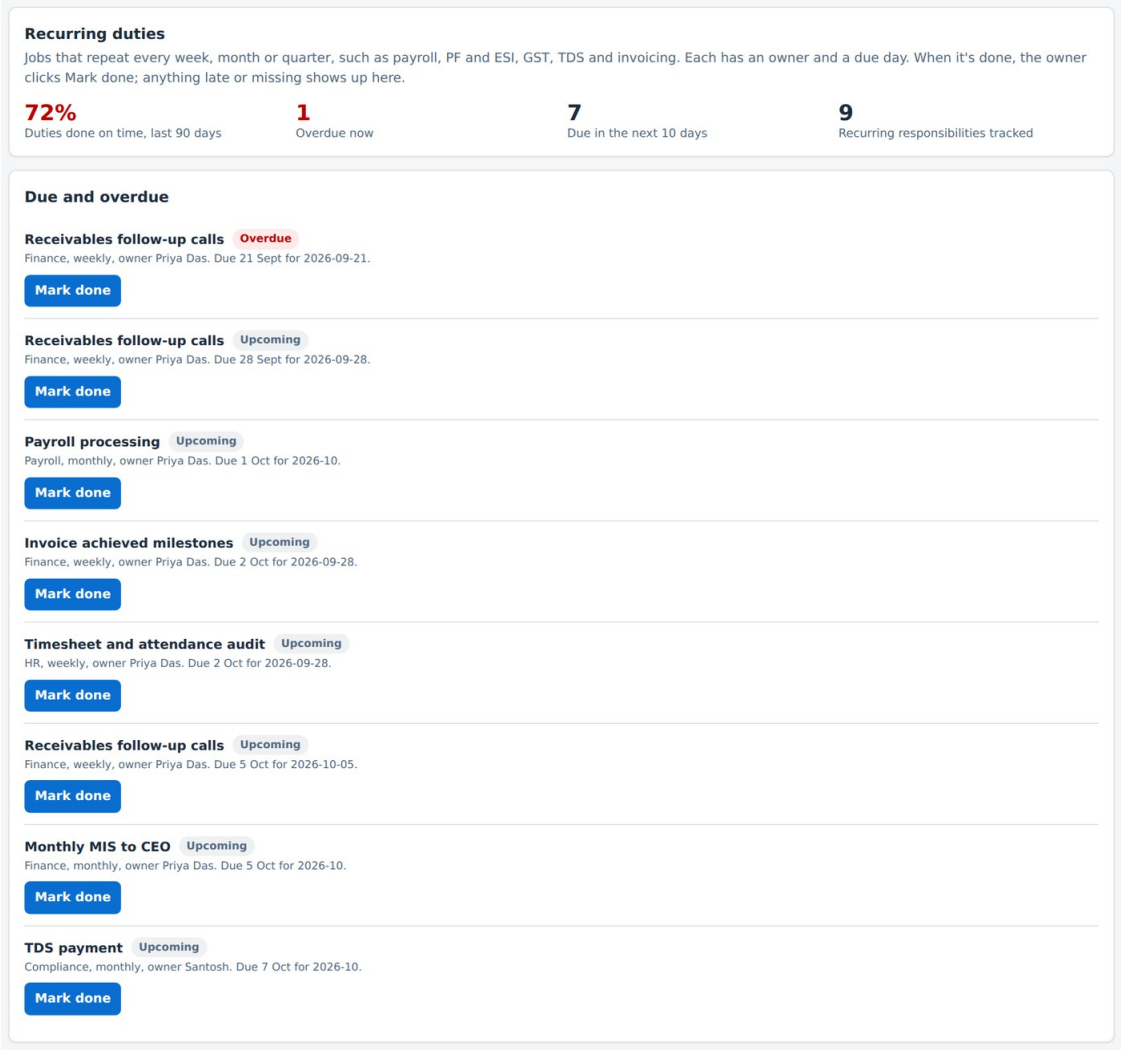

Operations: recurring duties, due and overdue items with Mark done

The **Operations** view runs the company's non-project work: recurring duties (monthly, quarterly, yearly) such as receivables follow-up, payroll processing, statutory filings and renewals, each with an owner and due date. **Mark done** rolls a recurring item to its next date. Its other tabs cover people and timesheet status, payroll, and invoicing and collections, each with a one-line description of what it is for.

15. Insights, weekly scorecard and client view

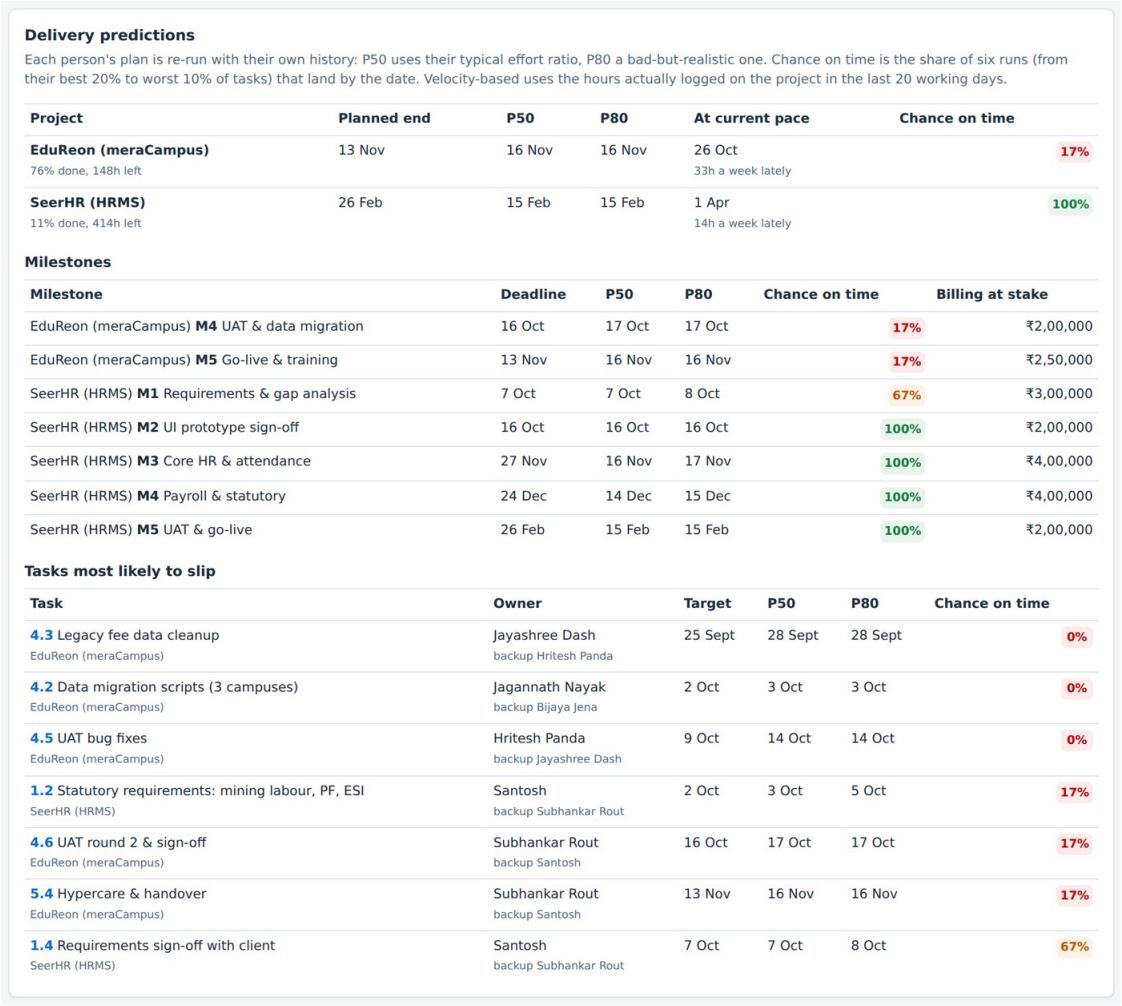

Delivery predictions

Each person's plan is re-run with their own history: P50 uses their typical effort ratio, P80 a bad-but-realistic one. Chance on time is the share of six runs (from their best 20% to worst 10% of tasks) that land by the date. Velocity-based uses the hours actually logged on the project in the last 20 working days.

Project	Planned end	P50	P80	At current pace	Chance on time
EduReon (meraCampus) 76% done, 148h left	13 Nov	16 Nov	16 Nov	26 Oct 33h a week lately	17%
SeerHR (HRMS) 11% done, 414h left	26 Feb	15 Feb	15 Feb	1 Apr 14h a week lately	100%

Milestones


Milestone	Deadline	P50	P80	Chance on time	Billing at stake
EduReon (meraCampus) **M4** UAT & data migration	16 Oct	17 Oct	17 Oct	17%	₹2,00,000
EduReon (meraCampus) **M5** Go-live & training	13 Nov	16 Nov	16 Nov	17%	₹2,50,000
SeerHR (HRMS) **M1** Requirements & gap analysis	7 Oct	7 Oct	8 Oct	67%	₹3,00,000
SeerHR (HRMS) **M2** UI prototype sign-off	16 Oct	16 Oct	16 Oct	100%	₹2,00,000
SeerHR (HRMS) **M3** Core HR & attendance	27 Nov	16 Nov	17 Nov	100%	₹4,00,000
SeerHR (HRMS) **M4** Payroll & statutory	24 Dec	14 Dec	15 Dec	100%	₹4,00,000
SeerHR (HRMS) **M5** UAT & go-live	26 Feb	15 Feb	15 Feb	100%	₹2,00,000

Tasks most likely to slip

Task	Owner	Target	P50	P80	Chance on time
4.3 Legacy fee data cleanup EduReon (meraCampus)	Jayashree Dash backup Hritesh Panda	25 Sept	28 Sept	28 Sept	0%
4.2 Data migration scripts (3 campuses) EduReon (meraCampus)	Jagannath Nayak backup Bijaya Jena	2 Oct	3 Oct	3 Oct	0%
4.5 UAT bug fixes EduReon (meraCampus)	Hritesh Panda backup Jayashree Dash	9 Oct	14 Oct	14 Oct	0%
1.2 Statutory requirements: mining labour, PF, ESI SeerHR (HRMS)	Santosh backup Subhankar Rout	2 Oct	3 Oct	5 Oct	17%
4.6 UAT round 2 & sign-off EduReon (meraCampus)	Subhankar Rout backup Santosh	16 Oct	17 Oct	17 Oct	17%
5.4 Hypercare & handover EduReon (meraCampus)	Subhankar Rout backup Santosh	13 Nov	16 Nov	16 Nov	17%
1.4 Requirements sign-off with client SeerHR (HRMS)	Santosh backup Subhankar Rout	7 Oct	7 Oct	8 Oct	67%

Delivery predictions: projects and milestones with forecast dates and chance of finishing on time; tasks most likely to slip

Insights looks ahead instead of back. Delivery predictions give each project and milestone a forecast date (P50 = even odds, P80 = 80% sure) and a chance of finishing on time, and list the tasks most likely to slip with their owners.

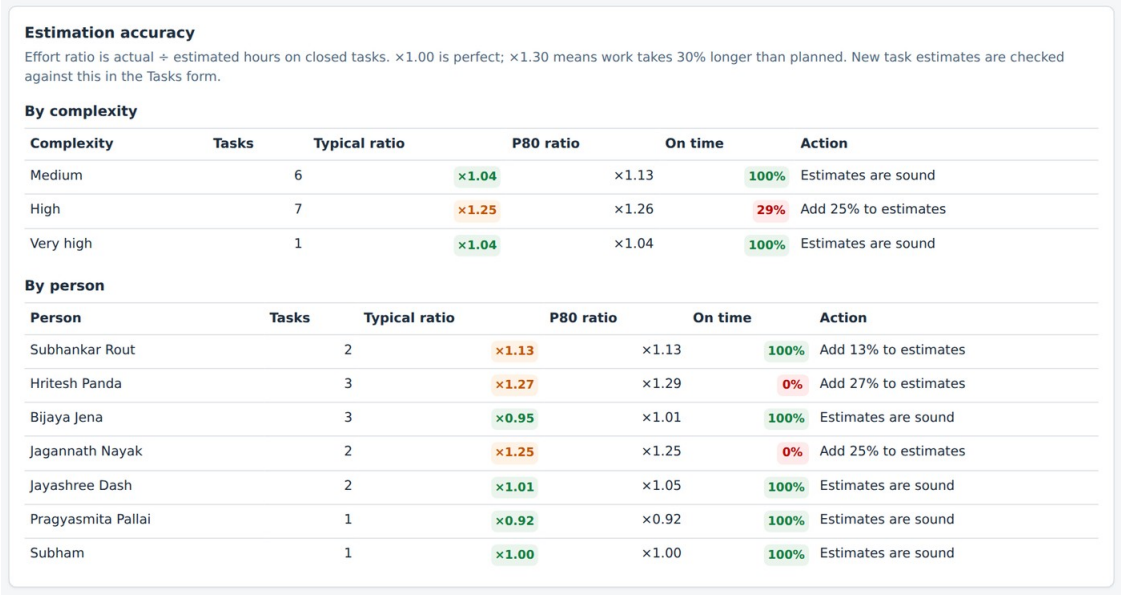

Estimation accuracy

Effort ratio is actual ÷ estimated hours on closed tasks. ×1.00 is perfect; ×1.30 means work takes 30% longer than planned. New task estimates are checked against this in the Tasks form.

By complexity


Complexity	Tasks	Typical ratio	P80 ratio	On time	Action
Medium	6	×1.04	×1.13	100%	Estimates are sound
High	7	×1.25	×1.26	29%	Add 25% to estimates
Very high	1	×1.04	×1.04	100%	Estimates are sound

By person

Person	Tasks	Typical ratio	P80 ratio	On time	Action
Subhankar Rout	2	×1.13	×1.13	100%	Add 13% to estimates
Hritesh Panda	3	×1.27	×1.29	0%	Add 27% to estimates
Bijaya Jena	3	×0.95	×1.01	100%	Estimates are sound
Jagannath Nayak	2	×1.25	×1.25	0%	Add 25% to estimates
Jayashree Dash	2	×1.01	×1.05	100%	Estimates are sound
Pragyasmita Pallai	1	×0.92	×0.92	100%	Estimates are sound
Subham	1	×1.00	×1.00	100%	Estimates are sound


Estimation accuracy by complexity and by person, with the suggested buffer

Estimation accuracy compares estimates to actual hours, by task complexity and by person, and suggests how much buffer to add to future estimates. It is how the team gets better at planning.

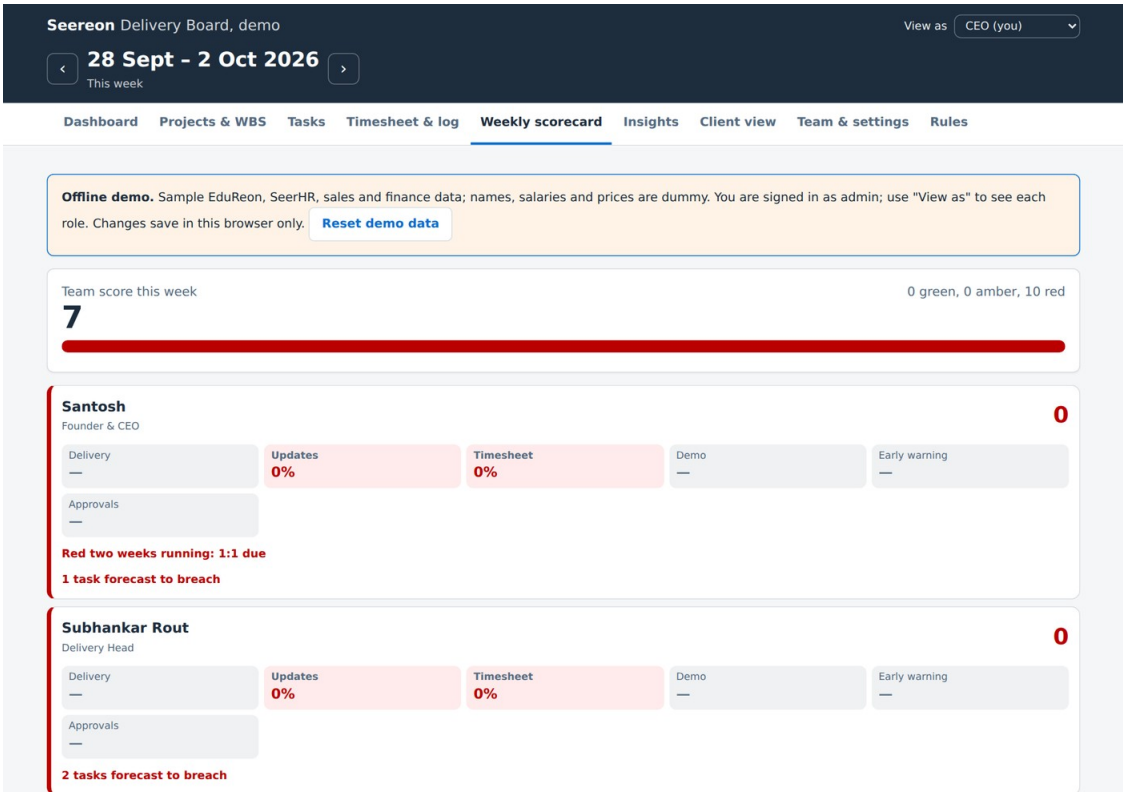

Weekly scorecard: each person's delivery score for the week


The **Weekly scorecard** gives each person a score for the week from on-time delivery, effort accuracy, daily updates and the Friday demo. Managers also carry their approval KPI (section 9).

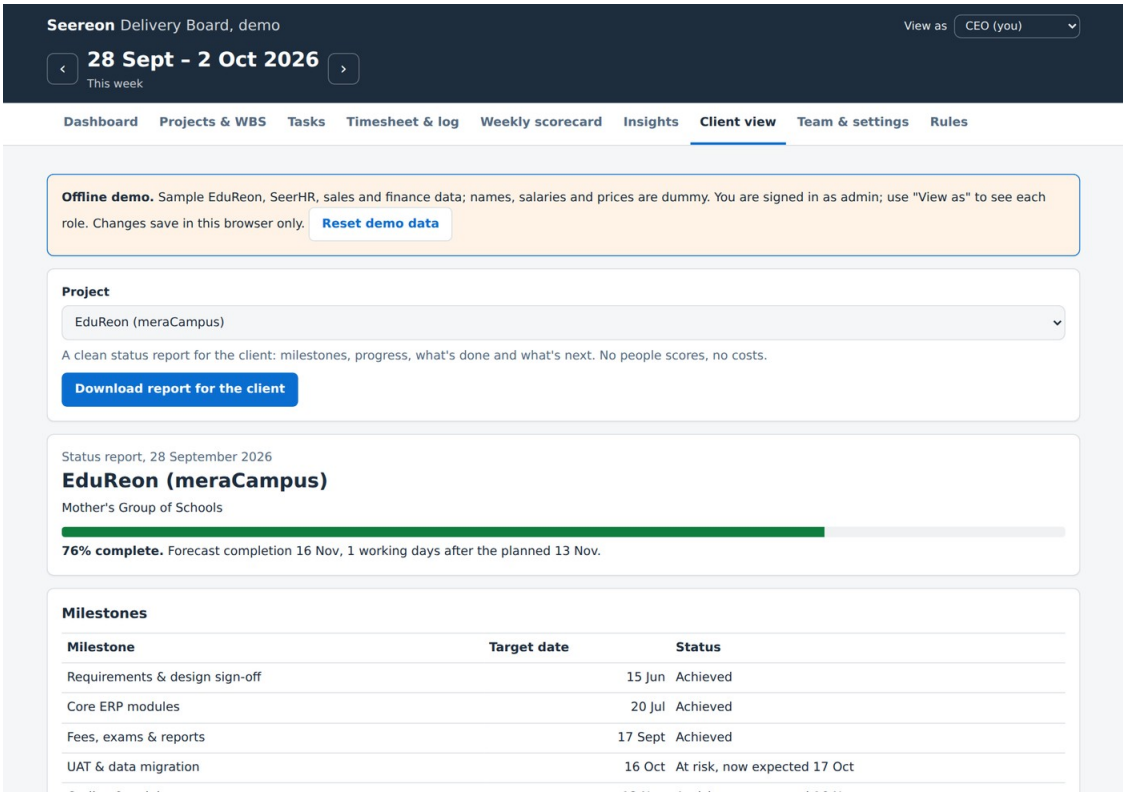

Client view: milestone progress, what was completed, what is coming, and decisions needed from the client

The **Client view** is a clean, money-free page per project to share with the client: milestone progress, what was completed in the last two weeks, what is coming in the next two, and the decisions or inputs needed from them.

16. Team and settings

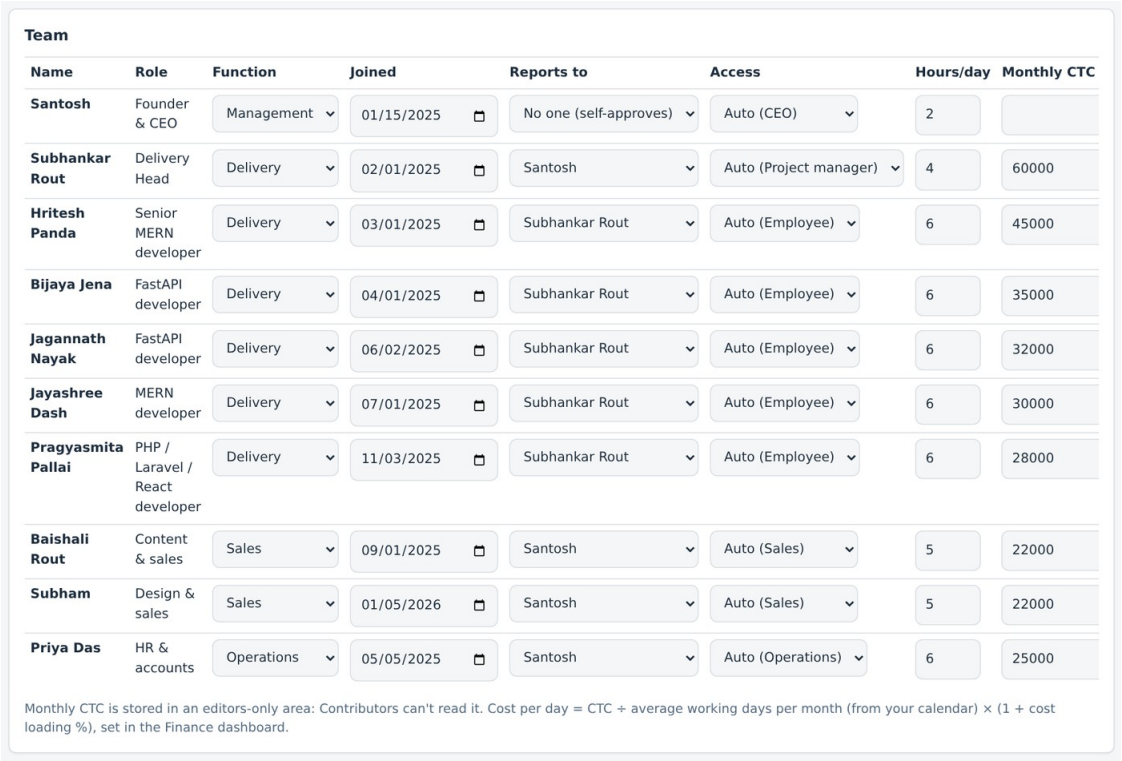


Team

Name	Role	Function	Joined	Reports to	Access	Hours/day	Monthly CTC
Santosh	Founder & CEO	Management	01/15/2025	No one (self-approves)	Auto (CEO)	2	
Subhankar Rout	Delivery Head	Delivery	02/01/2025	Santosh	Auto (Project manager)	4	60000
Hritesh Panda	Senior MERN developer	Delivery	03/01/2025	Subhankar Rout	Auto (Employee)	6	45000
Bijaya Jena	FastAPI developer	Delivery	04/01/2025	Subhankar Rout	Auto (Employee)	6	35000
Jagannath Nayak	FastAPI developer	Delivery	06/02/2025	Subhankar Rout	Auto (Employee)	6	32000
Jayashree Dash	MERN developer	Delivery	07/01/2025	Subhankar Rout	Auto (Employee)	6	30000
Pragyasmita Pallai	PHP / Laravel / React developer	Delivery	11/03/2025	Subhankar Rout	Auto (Employee)	6	28000
Baishali Rout	Content & sales	Sales	09/01/2025	Santosh	Auto (Sales)	5	22000
Subham	Design & sales	Sales	01/05/2026	Santosh	Auto (Sales)	5	22000
Priya Das	HR & accounts	Operations	05/05/2025	Santosh	Auto (Operations)	6	25000

Monthly CTC is stored in an editors-only area: Contributors can't read it. Cost per day = CTC ÷ average working days per month (from your calendar) × (1 + cost loading %), set in the Finance dashboard.

Team: each person's role, function, joining date, reports-to, access level, hours per day and monthly CTC

Team holds everyone who uses the board: name, role, function, joining date, who they report to (this decides who approves their timesheet), access level (which decides their dashboard view), working hours per day and monthly CTC (visible to the CEO only; it drives cost per hour and payroll).

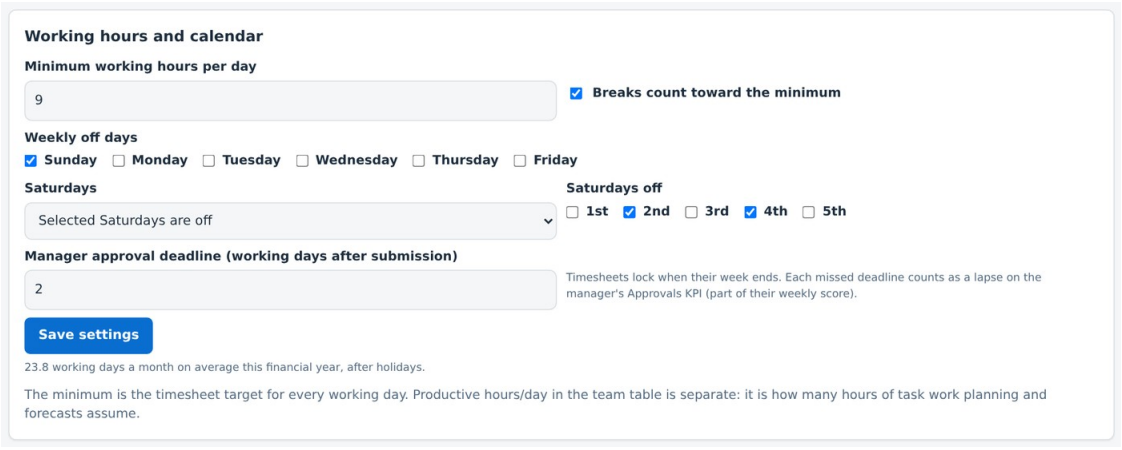

Working hours and calendar

Minimum working hours per day

9

Breaks count toward the minimum

Weekly off days

Sunday **Monday** **Tuesday** **Wednesday** **Thursday** **Friday**

Saturdays

Selected Saturdays are off

Saturdays off

1st **2nd** **3rd** **4th** **5th**

Manager approval deadline (working days after submission)

2

Timesheets lock when their week ends. Each missed deadline counts as a lapse on the manager's Approvals KPI (part of their weekly score).


Save settings

23.8 working days a month on average this financial year, after holidays.

The minimum is the timesheet target for every working day. Productive hours/day in the team table is separate: it is how many hours of task work planning and forecasts assume.


Working hours and calendar: minimum hours, whether breaks count, weekly off days, which Saturdays are off, and the approval deadline

Working hours and calendar sets the company rules everything else calculates from: minimum hours per working day (9), whether lunch and tea breaks count toward it, the weekly off (Sunday), which Saturdays are off (2nd and 4th), and the manager's approval deadline in working days (2). The holiday calendar below it lists public holidays for the year.

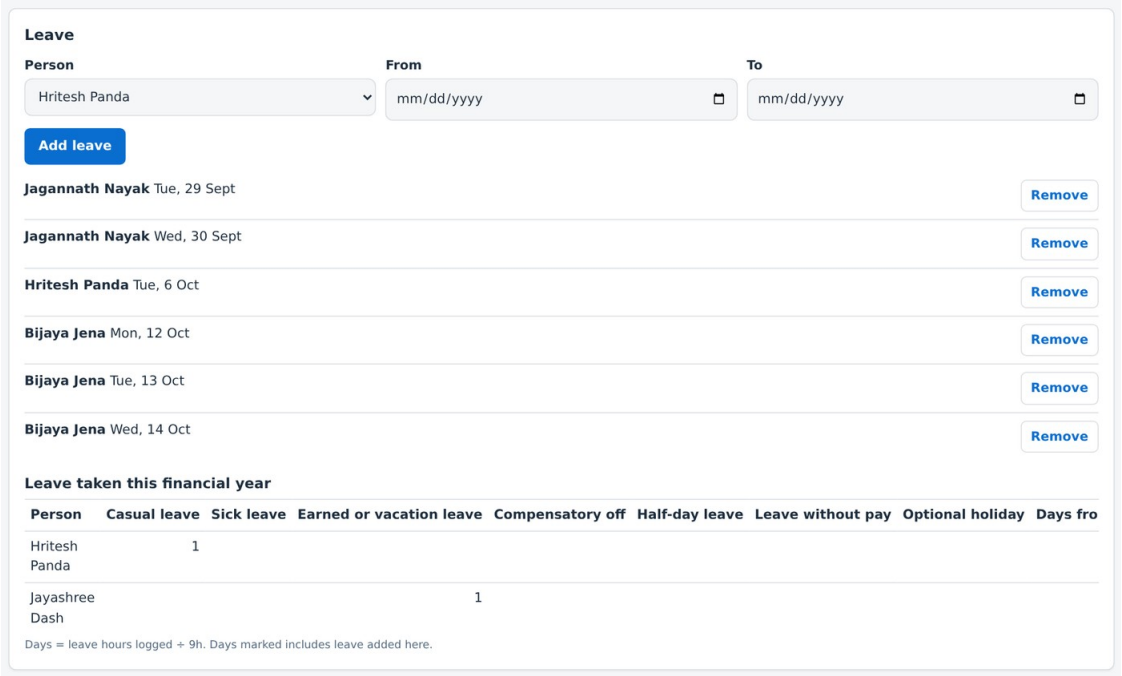

Leave: record leave for a person and date range, and leave taken this financial year by type

Leave records leave for a person and a date range. Leave also comes in from the timesheet's leave row, so either route keeps both in step. The table shows leave taken this financial year by type (casual, sick, earned, compensatory, leave without pay).

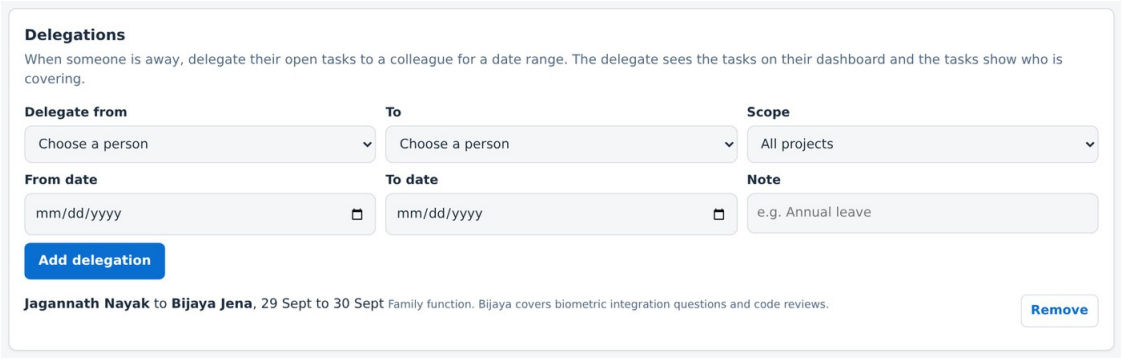

Delegations: hand approvals to another person for a date range

Delegations let a manager hand their approvals (and optionally their task follow-ups) to another person for a date range, typically while on leave. Approvals made by the delegate count toward the delegate's approval KPI.

The SaaS version groups every company setting in one place, with the default and allowed range shown next to each; the Technical Design (section 15) lists them all.

17. Rules and KPI definitions

The Rules tab is the board's rulebook: the non-negotiable working rules, how the weekly score is built, how the schedule forecast works, and the consequences of breaking a rule. Every number on the board is defined here, so nobody argues about what a metric means.



KPI definitions

On-time delivery	Completed tasks finished on or before the target end date ÷ completed tasks.
Effort ratio	Actual hours ÷ estimated hours, median of completed tasks. ×1.00 = spot on; ×1.30 = work takes 30% longer than estimated; ×0.80 = estimates are padded. Above ×1.3 means chronic underestimating.
Markup vs margin	Both use the same profit (price − cost). Markup divides it by cost; margin divides it by price. 60% markup = 37.5% margin. Margin can never reach 100%; markup can.
Sales variable	Paid only in a month where the salesperson's closed deals reach their target (default = their monthly CTC).
Task statuses	New, Selected for development, In development, Unit testing, Functional testing, UAT, Waiting for feedback, On hold, Blocked, Completed. Moving to a testing stage raises progress to at least 60% (unit), 75% (functional) or 90% (UAT).
Critical task	The task that sets its milestone's deadline, i.e. the latest planned end in the milestone, plus any task whose dependents would push it. Float is how many working days a task can slip before it moves its milestone.
Working days	Every day except the weekly off days and Saturday rule set in Team & settings, minus company holidays. Optional holidays are taken as leave.
Resource allocation	Each resource is allocated to a milestone (or all milestones) with a required start and end date. The same person can have several rows, one per milestone.
Resource cost	Cost per day × allocation % × working days between the resource's start and end dates. Cost per day = monthly CTC ÷ average working days per month × (1 + cost loading).
Milestone deadline	Always the target end date of the milestone's last task. It moves only when a task's target date moves.
% complete	Earned hours ÷ total estimated hours. Earned = estimate × progress %.
SPI	Schedule performance: earned hours ÷ planned hours to date. Below 1.0 means behind plan.
CPI	Effort performance: estimated ÷ actual hours on completed tasks. Below 1.0 means tasks cost more effort than planned.
Schedule variance	Working days between planned end and forecast end. Positive means late.
Utilisation	Forecast hours due in the next 10 working days ÷ capacity.
Timesheet	Hours logged this week ÷ available hours (capacity minus holidays and leave). Leave rows count toward the target; a full-day leave row marks the day as leave.
Scope growth	Approved change-request hours ÷ baseline effort.
Baseline variance	Working days between a milestone's baseline deadline and its current deadline.
Markup	(Price − cost) ÷ cost. Cost = Σ(resource cost per day × man-days) + maintenance, where cost per day = CTC ÷ average working days per month × (1 + cost loading). Additional costs and contingency are added on top. Positive is profit, negative is loss.
Planned margin	(Price − planned cost incl. contingency) ÷ price, from the saved costing.
Projected margin	Fixed cost: contract value (price + approved CRs) − projected cost. A resource allocated up to a milestone's deadline stays on until the milestone's forecast or actual end: a late milestone adds breach cost, an early one saves cost. Unplanned people's time is added; contingency stays as cost until the project closes. Time & resources: billing and cost follow logged hours.
Actual margin to date	(Earned revenue − cost to date) ÷ earned revenue, where earned revenue = contract value × % complete.
P50 / P80 date	The forecast re-run using each person's typical (median) and worst-realistic (80th percentile) effort ratio from their closed tasks. Chance on time is the share of six such runs that finish by the target.
Performance trend	Weekly average of on-time delivery and timesheet discipline over 12 weeks; direction compares the latest six weeks with the six before.
Gross margin	(Contract value − forecast cost at completion) ÷ contract value. Margin is on revenue; markup is on cost.
Net margin	(Revenue billed − payroll − overheads − other expenses) ÷ revenue billed, for the period.
DSO	Days sales outstanding: receivables ÷ average daily billing over the last 90 days.
Runway	Cash balance ÷ (monthly burn − recurring monthly income).

KPI definitions: on-time delivery, effort ratio, markup and margin, sales cycle, cost per hour, working days and every other measure the board uses

The measures people ask about most:

Measure	Plain meaning
On-time delivery	Share of tasks finished on or before their due

Measure	Plain meaning
	date
Effort ratio	Actual hours ÷ estimated hours; above 1.0 means it took longer than planned
SPI	Schedule performance: work done ÷ work planned by today; below 1.0 means behind
Margin	Profit ÷ revenue
Markup	Profit ÷ cost (a 50% markup is a 33% margin)
Cost per hour	Monthly CTC ÷ (working days × minimum hours)
Win rate	Deals won ÷ (won + lost)
Approval KPI	Approvals made on time; late or missed approvals count against the manager
P50 / P80 date	The date a task or milestone has an even or 80% chance of finishing by

When the board and a spreadsheet disagree, the definitions here decide which is right.
